

1- Please process ECG's progress with the cabanas buildings blocks at Zone 1K as a top-priority :-

- Block 1: (6 units BC)
- Block 2: (8 units BC)
- Block 4: (14 units Jr.BC)
- Block 5: (15 units Jr.BC)
- Block 6: (16 units Jr.BC)

2- Please check the structural Statical system.

3- Please work on the latest files of the prototypes already sent to ECG.

4- Please study the suitable indoor locations for Electrical Water Heaters; (no instant are allowable).

5- Please study/check the outdoor locations for both smart Electrical meters and Water meters; (as proposed by our international consultant GP&P) considering the required access from outside will be needed from Tatweer Misr's FM team during the future operation.
also, please consider a separate metering for each key.

6- Please study the locations for the indoor Electrical Panels (Lighting & Low Current) and to be coordinated with ID consultant.

7- Please study the locations of the Internal & External AC units (back to back as much as possible is preferred).
However, please check the proposed by our international consultant GP&P considering the external units to be hanged with minimum 2.10 clear head below.

D. BAY

NORTH COAST EGYPT

ECG – Concept Design Review Report

01 BC- BEACH CABIN (40 sq.m)

Typical Comments for 01 BC- (50 sq.m)



ECG **مجموعة الاستشارات الهندسية**
ENGINEERING CONSULTANTS GROUP

OCTOBER 1, 2021

- 1- Please validate all issues considering the marketing material for the project
- 2- No mirror units following the contracts with our clients, please refer to the latest master plan rev. 21

General Comment:

Appreciate to have all ECG's future comments in an editable PDF format with a good resolution

No big issue. However, to be coordinated with ID consultant

ID consultant to further check




Spacing between door & window is too small, when fully open door leaf & window sash will crash

Towel rail location is impractical / non-functional

- Relation between wardrobe & wall is critical, unless materials are carefully selected & accurately implemented flush
- Built-in wardrobe sides would contribute cost reduction, as volume of wood component is lesser & ensures continuation of the wall finish
- This's applicable in case of fully furnished units marketing

All residential units are fully finished scope only with no furniture. Please keep as it is with no wall nib

All intermediate terraces' separation walls to be same as shown in the marketing movie

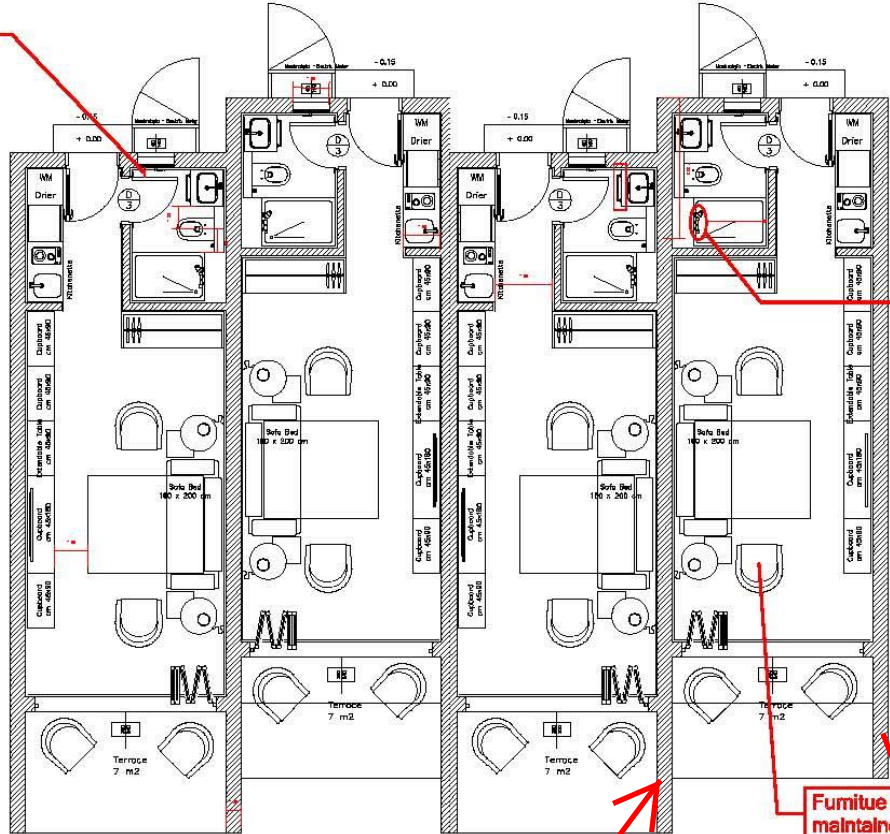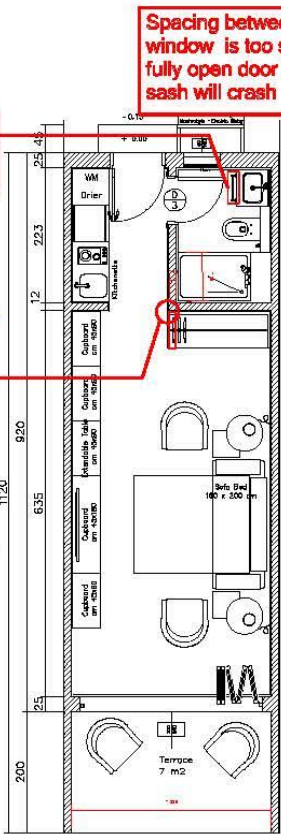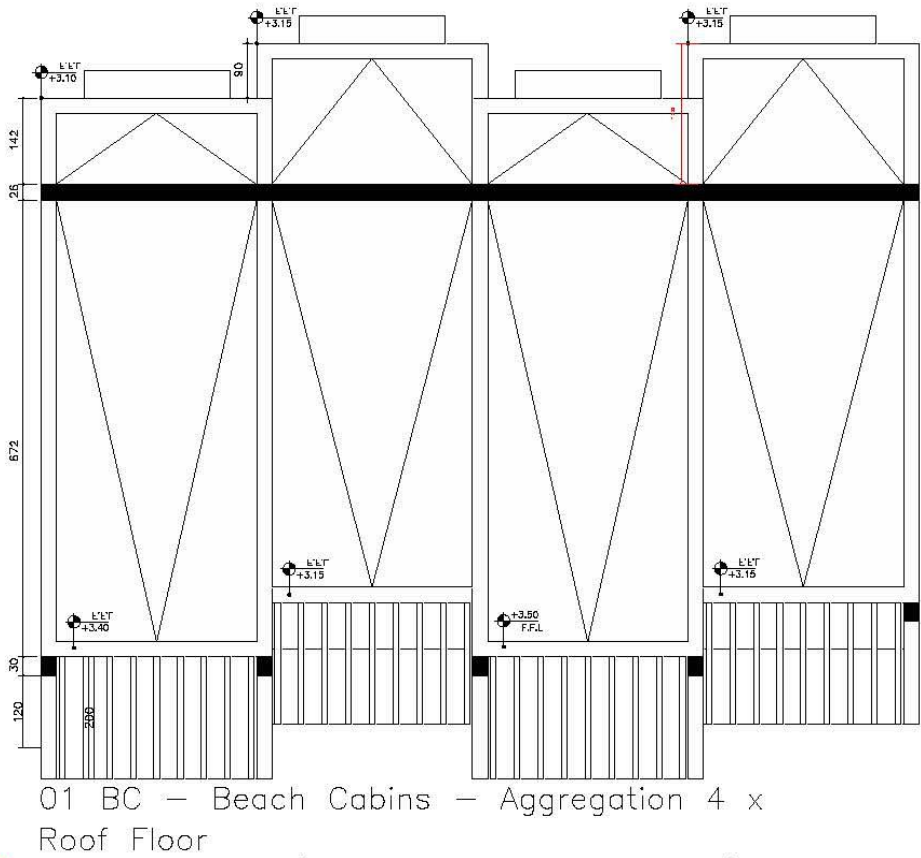

Ok, please proceed

D.Bay
01 BC - Beach Cabin
40 m2

D.Bay
North Coast | Egypt

Owners of the project

Tatweer Miar

Project Manager

Address: 25, Avenue Al Tahrir, Heliopolis, Cairo, Egypt

Mobile: 011 4552 8884 - 3.png

Project Code: 214849

Designers

Architectural, interiors, landscape and structural design

Poluffo & Partners

Headquarters

Poluffo & Partners S.p.A.

Via S. Andrea 10 - 00187 Roma, Italy

Tel: +39 06 4781100

Fax: +39 06 4781101

Studio Lab

Studio Lab Interior

Poluffo & Partners S.p.A.

Via S. Andrea 10 - 00187 Roma, Italy

Tel: +39 06 4781100

Fax: +39 06 4781101

- If shower head is relocated at the opposite side, there'll be potential for built in seat or shelves to replace
- At the same time, this will facilitate manual test of water temp. prior to getting into shower tray

Please to be coordinated with ID consultant

- Furniture layout needs to be revisited to enhance functionality, e.g. in case sofa bed is maintained at sleeping mode,
- > How to provide nice seating arrangement near window
- > How to use extendable table comfortably & without interrupting circulation

