

DAMAC DATA CENTRES

PMWeb Implementation & Day 0–2 Capability Framework

Project Controls · Cost Management · Commercial · Procurement

Design Delivery · Construction · Handover · ERP Integration

Day 0	Day 1	Day 2
Site Selection & Investment	Design & Build	Customer & Operations

PMWeb Scope at a Glance

Cost & Budget Management

Commercial & Contract

Schedule & Project Controls

Design & Construction Delivery

Procurement & Tendering

Handover & Closeout

ERP Integration (Oracle)

Portfolio Dashboards & Reporting

Today's Agenda

PMWeb capabilities across the full Day 0 → Day 1 → Day 2 lifecycle

01

Day 0 — Site Selection & Project Initiation

PMWeb role: Project Setup, Estimation, Portfolio Configuration

02

Day 1 — Cost & Budget Management

Budget request/approval, budget revisions, cashflow, cost forecasting

03

Day 1 — Commercial & Contract Management

Commitments, payment certificates, change management, variations

04

Day 1 — Schedule & Project Controls

Schedule builder, baseline, EVA, risk management

05

Day 1 — Design & Construction Delivery

Transmittals, submittals, RFIs, NCRs, HSE, site management

06

Day 1 — Procurement & Tendering

Procurement strategy, vendor prequalification, tendering, award

07

Day 1 — Handover & Closeout

O&M manuals, snagging, TOC, lessons learned

08

ERP Integration & Portfolio Reporting

Oracle ERP integration, KPI dashboards, data migration

PMWeb in the DAMAC Ecosystem

Where PMWeb sits, what it owns, and how it connects to Oracle ERP, Autodesk ACC, and the Data Lake

Oracle ERP

Financial Backbone

- Consolidated cost codes (CBS)
- Program/project budget approval
- POs triggered from PMWeb BOQ
- IPC / progress payments
- AP/AR · GL · Fixed Assets

PMWeb (PMIS)

Project Control Hub — Golden Record for:

- Full BOQ: items, quantities, rates
- WBS, activity schedule, baseline
- EVA: SPI, CPI, EAC, ETC
- Procurement & commercial records
- All project forms & workflows

Autodesk ACC

Design Source of Truth

- BIM model · IFC drawings
- RFI / submittal / document control
- Clash detection · as-built models
- BOQ quantities linked to BIM
- Material data sheets (MDS)

↓ Centralized Data Lake + Azure BI — feeds from all three platforms: KPIs, cost, schedule, ESG, capacity ↓

Day 0 — Project Initiation & Estimation

PMWeb scope: Portfolio setup, project registration, cost estimation before design commences

DAMAC Capability Map: Site Identification & Evaluation · Financial & Technical Evaluation · Concept & Project Initiation · Land Valuation & Cost Analysis



Software Setup & Portfolio Configuration

- Portfolio hierarchy setup — Program → Project level
- Cost Codes / CBS configured to DAMAC's chart of accounts
- Users, Roles & Access Rights — RBAC per function
- Company/vendor registry with pre-qualification status
- Currencies setup with conversion rates
- Project master record creation at Gate 0



Project Initiation (Plans – Initiatives)

- Initiatives module — formal project registration
- Project profile: site, Tier, MW capacity, Uptime target
- Initiative approval workflow (Gate 0 business case)
- Initiatives register dashboard — all sites, all stages
- Links to Financial & Technical Evaluation deliverables



Estimation (Plans – Estimates)

- Project Estimation forms and workflows tailored
- Benchmark Estimation — \$/kW parametric benchmarks
- Estimation assemblies by CBS category (electrical, mechanical, ICT)
- OOM → SD → DD accuracy improvement tracked ($\pm 30\%$ → $\pm 10\%$)
- Estimation summary reports for board approval
- Feeds Oracle ERP consolidated budget at Gate 1

Day 1 — Cost & Budget Management

PMWeb owns the full BOQ, work packages, budget lifecycle, and cashflow — ERP receives consolidated cost codes only

DAMAC Capability Map: Project Level Budgeting · BOQ & Work Package Management · Finance Budgeting · Cost Control & Forecasting

Budget Management

Budget Request & Approval

Tailored budget development forms with multi-tier approval workflow

Budget Change Request

Revision management and approval — with reason codes and impact assessment

Budget Transfer Request

Reallocation between CBS codes with dual-approval workflow

Budget Reporting — Live

Live Budget vs Cost vs Forecast dashboard with drill-down to BOQ line level

Cost Management & Cashflow

Change Events / Early Warnings

Potential cost risk register — flagged before they become variations

Cashflow Management

Custom cashflow criteria and forms aligned to DAMAC financial policies

Program/Portfolio Report

Multi-project cost dashboard: budget, commitment, actual, forecast

Trending Cost Estimation

Trend analysis report tracking cost trajectory across all work packages

System boundary: PMWeb holds full BOQ detail (quantities, rates, work packages, EVA). Oracle ERP receives consolidated cost code totals only — for budget approval, PO issuance, and payment processing.

Day 1 — Commercial & Contract Management

Full payment certification lifecycle, change management, and variation control within PMWeb

DAMAC Capability Map: Award & Contract · Build, Test & Commission · Finance — IPC, Accounts Payables, Supplier Management

Payment Certification

Advance Payment Certificate — with bond and guarantee validation checks

Interim Payment Application (IPA) — multi-currency; contractor/vendor self-submission

Interim Payment Certificate (IPC) — advance recovery, retention, budget vs payment check

Partial / Milestone Completion Certificate — service vendor payment on milestone basis

Miscellaneous Invoices — non-commitment related payments

Material on Site Payments — site-stored materials payment tracking

Final Account Statement — custom Final Account forms and approval workflow

Change Management

Employer Instruction (EI)

Formal EI form integrated with Change Management workflow

Engineer's Instruction (ENG)

Instruction form for site-level engineer instructions

Change Notice / Request

Change requests originated by vendor, contractor, or employer

Potential Change / Anticipated Variation

Employer-originated early change events

Approval of Change

Multi-tier approval workflow per DoA

Variation Order (VO) Approval

Full VO lifecycle — negative variations supported

Provisional Sums

Commitment management for provisional sum drawdown

Reports: Payment Certificates Log · Change Management Log · Cashflow Report · Provisional Sum Award Status · Trending Cost Estimation

Day 1 — Schedule & Project Controls

PMWeb owns the WBS, schedule baseline, EVA, risk register, and meeting minutes

DAMAC Capability Map: Project Planning & Scheduling · WBS · EVA · Critical Path · Risk & Mitigation Strategies

Schedule Management

Schedule Builder (Schedules module)

Configured for DAMAC schedules; imports Primavera P6 / MSP database

Baseline Management

Baseline setup and versioning — schedule freeze at each phase gate

WBS — Activity Sequencing & Resources

WBS 1–5 levels; resource assignment; critical path analysis; resource leveling

Earned Value Analysis (EVA)

BCWS, BCWP, ACWP per WBS; SPI / CPI trend; EAC / ETC forecasts

What-if Scenario Planning

Scenario modelling for recovery options; lookahead reports

Schedule Progress Dashboard

Live S-curve; milestone adherence; portfolio-level consolidated view

Risk Management & Meeting Minutes

Risk Registration

Risk forms with probability × impact matrix, risk categories, and mitigation plans

Risk Management Plans

Assigned risk owners; residual risk tracking; Monte Carlo contingency modelling

Risk & Issues Register

Live dashboard — Top 10 risks by exposure; heat map; status tracking

Meeting Minutes

Structured meeting minutes forms; action items; approval and distribution workflows

Schedule Risk Dashboard

Linked from risk register to schedule — critical path risk flags

Day 1 — Design & Construction Delivery

PMWeb manages all project communication, submittals, site execution forms, and HSE records

DAMAC Capability Map: Standardized Design & Engineering · Shop Drawings · IFC Drawings · Construction Management · HSE Management · Build, Test & Commission

Design Delivery

Transmittals

Configured per DAMAC nomenclature and document numbering system

Submittals

Design submittal register with revision control and distribution workflow

Correspondences

Formal correspondence management with read/respond audit trail

Design Review Process

BlueBeam add-on integration (if opted); mark-up and comment tracking

Design Approval Process

Staged design review workflow: SD → DD → CD with approval sign-offs

Design Change Request

Design change management integrated into cost change workflow

Construction Delivery & HSE

Shop Drawing & Material Submittals

Submittal register with vendor/contractor submission workflows

Requests for Information (RFI)

RFI log with response SLA tracking; linked to design drawings

Site Observation Reports

Inspection and observation records with photographic evidence

Non-Conformance Reports (NCR)

NCR register with root cause, corrective action, and close-out tracking

Safety Violation & Accident Reports

HSE incident forms with severity classification and investigation workflow

Daily Reports & Inspection Requests

Daily progress records; inspection request and approval forms

Site Management (Offline / Adaptive Forms)

Mobile forms for offline site use — syncs when online

Day 1 — Procurement & Tendering

End-to-end procurement lifecycle managed in PMWeb — from strategy through vendor award

DAMAC Capability Map: Procurement Strategy · Category Management · Pre-Tendering · Tendering & Evaluation · Award & Contract · Sourcing Strategy · Single vs Multi-Vendor

Procurement Strategy

- Procurement Strategy Form — tailored per DAMAC requirements
- Bid package module setup — single vs. multi-vendor decisions
- Procurement strategy approval workflow

Vendor Prequalification

- Vendor Pre-Qualification Form — tailored with DAMAC-specific criteria
- Vendor approval module — TIA-942 approved vendor list status
- Vendor Feedback forms — post-delivery performance scoring

Tendering Process

- Expression of Interest (EOI) — custom form and distribution
- Tender Issue — documentation compilation and issue to bidders list
- Tender Clarification (RFC) — internal collation and bidder feedback
- Tender Evaluation — commercial and technical scoring (separate reviewer)

Award & Contract

- Award Recommendation Report — multi-function input, DoA approval workflow
- Commitment Registration — multi-currency, split contract support
- Commitment management — revisions, updates, tracking against BOQ
- Procurement Team Dashboard — status, pipeline, spend-to-date

Day 1→2 — Handover & Closeout

PMWeb manages the full handover lifecycle — from snagging through TOC to operational readiness

DAMAC Capability Map: CEWA QA & Commissioning · Asset Tagging & CMMS Setup · Lessons Learnt & Takeover Certificate · Customer Delivery Completion — AS BUILT Models



O&M Manuals & As-Built Models

- Handover documentation forms — structured O&M manual submission workflow
- AS BUILT model receipt — linked to Autodesk ACC as-built drawings
- O&M Manual Log / Status Report — tracking completeness per system



Taking Over Certificate (TOC)

- TOC form and approval workflow — linked to final account process
- Partial / Section TOC — zone-by-zone handover for phased delivery
- Closeout Tracker Dashboard — all handover milestones and completion %



Snagging / Punchlist Management

- Snagging forms — item creation, assignment to contractor, priority classification
- Punchlist closeout workflow — inspection, re-inspection, acceptance sign-off
- Snagging Log Report — open items, responsible party, target dates



Lessons Learned & Closeout

- Lessons Learned form — categorised by phase, system, risk type
- Lessons Learned database — searchable across all DAMAC DC projects
- Feeds Gate 6 Operations Handover — informs Day 2 CMMS and MOP/SOP setup

ERP Integration & Data Migration

PMWeb ↔ Oracle ERP integration — defined data flows with clear system-of-record boundaries

DAMAC Digital Ecosystem: Integration Phase 1 — Oracle ERP + PMWeb as Priority Integration; Data Migration from Current Systems

Integration Architecture — Data Flows

Oracle ERP → PMWeb

Approved consolidated budget → PMWeb cost baseline (by WBS/cost code)

PMWeb BOQ → Oracle ERP

Approved BOQ line → triggers Oracle ERP Purchase Order (PO) against consolidated cost code

PMWeb IPC → Oracle ERP

Certified Payment → Oracle ERP IPC payment processing → AP/supplier payment

Oracle ERP → PMWeb

Actuals (payments made) → PMWeb cost-to-date reconciliation and EAC update

PMWeb → Data Lake

Cost, schedule, procurement, EVA data → Centralized Data Lake → BI dashboards

Data Migration

Data Alignment & Analysis

Review existing systems and data structures; define migration strategy and templates

Extraction & Transformation

Extract from current systems; transform to PMWeb-compatible format

Migration to PMWeb

Load validated data; number of projects to be confirmed at mobilisation

Integration Rule: The BOQ never enters Oracle ERP. PMWeb holds the full BOQ. Oracle ERP holds the consolidated cost code, the approved budget, and processes the PO and payment only.

Portfolio Dashboards & Reporting

PMWeb delivers custom-developed dashboards across all functional areas — from site to boardroom

Development type: Custom Development — all dashboards are designed and built to DAMAC's specific reporting requirements

Portfolio & Cost

- Portfolio Level KPI Dashboard (monitoring all projects)
- Live Budget vs Cost vs Forecast — drill down to BOQ
- Program/Portfolio Cost Dashboard
- Cashflow Report with S-curve

Commercial

- Payment Certificates Log & Status
- Cashflow and drawdown reporting
- Provisional Sum Award Status
- Change Management Log & Status

Schedule & Risk

- Schedule Progress Dashboard (S-curve, milestone)
- Program/Portfolio Schedule Report
- Risk & Issues Register Dashboard
- What-if scenario comparison

Design & Construction

- Design Submission Status Report
- Design Management Dashboard
- Submittal & Transmittal Log/Status
- NCR · RFI · Inspection Status Reports

Procurement

- Procurement Packaging Strategy Report
- Vendor Prequalification Status
- Tendering Process Status Report
- Procurement Team Dashboard


Handover & HSE

- O&M Manual Log / Status Report
- Snagging Log & Closeout Tracker
- HSE Report (Safety, Accidents, NCRs)
- Department Workstations (up to 3 functions)

Implementation Approach & Next Steps

How we mobilise the PMWeb implementation alongside the Day 0→1→2 framework delivery

BRD → Configuration → Customisation → Data Migration → Integration → Training → Go-Live → Support

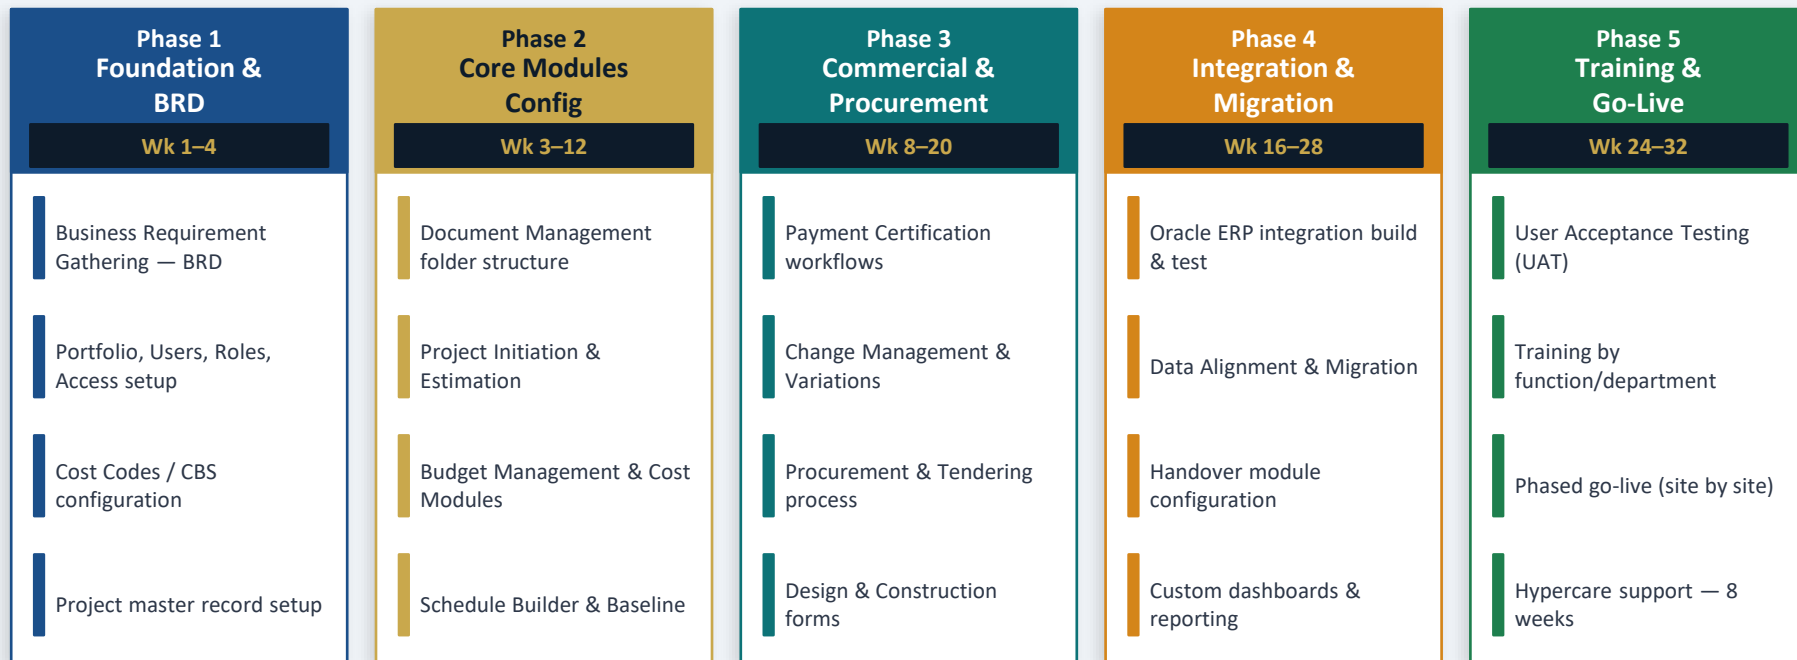

Implementation Team: Project Manager · SME Consultant · Functional Consultant(s) · Developer · Integration Consultant · CMCS Staff

PMWeb — Built for DAMAC Scale.

*Full project control lifecycle from Gate 0
through Operations — one platform,
clear boundaries, unified Data Lake.*

Day 0 · Day 1 · Day 2

Cost · Commercial · Schedule · Procurement · Handover

What PMWeb Delivers for DAMAC

Cost Control

- Full BOQ with quantities, rates, work packages
- Budget lifecycle: request → revision → transfer → close
- Live Budget vs Forecast dashboard — ERP reconciled

Commercial Discipline

- End-to-end payment certification (7 certificate types)
- Change management: EI, ENG, VO, Provisional Sums
- Commitment management with multi-currency support

Schedule & Risk Integrity

- P6/MSP import, WBS baseline, EVA (SPI/CPI/EAC)
- Risk register with Monte Carlo contingency modelling
- Meeting minutes, action tracking, phase gate controls

Procurement & Handover

- Vendor prequalification → tendering → award → contract
- O&M manuals, snagging, TOC, lessons learned
