

SHUROOQ PMWeb Implementation Proposal

12/4/2018

PMWeb Scope of Work

A. Implement The Following PMWeb Modules

1. Companies
2. Projects
3. Actions
4. Cost Breakdown Structure
5. Financial Periods
6. Budget
7. Budget Requests
8. Commitments
9. Potential Change Orders
10. Change Orders
11. Progress Invoices
12. Document Management Repository
13. Custom Forms – Stakeholder
14. Custom Forms – Schedule Track

15. Custom Forms – Risk

16. Custom Forms – Issues

17. Custom Forms – Nominated Subcontractors

B. Output Forms, Reports and Dashboards

1. Budget Request Form
2. Change Order Form
3. Variation Order Form
4. Progress Invoice Report
5. Cost Report/Commitments Log
6. Nominated Subcontractors Form
7. Project Charter Report
8. Dashboard - Project
9. Dashboard – Projects Portfolio
10. Dashboard – Projects Analysis

C. Training on the Above Modules and Reports

CMCS Scope of Services

- 1. Initially CMCS will provide one day overview training of PMWeb modules to be implemented at Shurooq. During this session, Shurooq will be given MS XLS templates which will be used by Shurooq team to collect the data to be added to PMWeb. CMCS team will be available to respond to Shurooq queries as it relates to how to complete those MS XLS files via email or phone.**
- 2. After one week, CMCS will conduct a one-day training on Companies, Projects, Action Item and Document Management Repository. This training will show Shurooq on how to add data to those modules. During this week, CMCS will create the document management system folders and subfolders based on the information provided by Shurooq.**
- 3. Also during this second week, CMCS will create the five custom forms as well as start developing the forms, reports and project dashboard. CMCS team will be available to respond to Shurooq queries as it relates to those modules via email or phone.**
- 4. The third week will include training on the cost modules for one-day. This training will show Shurooq on how to add data to those modules. CMCS team will be available to respond to Shurooq queries as it relates to those modules via email or phone.**

- 5. The fourth week will start with a one-day training to show Shurooq team on how to use the custom forms. This one day training will also cover PMWeb admin training and how to create workflows. This training will show Shurooq on how to add data to those custom forms. CMCS team will be available to respond to Shurooq queries as it relates to those modules via email or phone.**
- 6. During the fourth week, CMCS will present the forms, reports and project dashboard with the data added for the project or projects added by Shurooq team.**
- 7. Weeks 5 and 6 will be used by CMCS to create the Projects Portfolio and Projects Analysis dashboards for which the final design will be agreed on with Shurooq during the elapsed 4 weeks.**

Financial Proposal



Module	Qty	List Price AED	U/M	Invoice Amt AED
Professional Services				
PMWeb Senior Consultant	3	19,536	WK	58,608
PMWeb Report Writer	5	9,768	WK	48,840
			Services AED	107,448
PMWeb University On Line Subscription - OPTIONAL				
PMWeb University On Line Subscription - OPTIONAL	1	18,400	Year	18,400
			Additional 4 Years	18,400
			Grand Total Services	125,848
			VAT	6,292
			Grand Total PMWeb AED	132,140

Payment Terms

- 1. 50% Advance Upon Award of Contract and balance 50% upon Completion of Services**
- 2. PMWeb University Year One Subscription Option is Highly Recommended but Not a Must**

Project Dashboard

Project Details



Construction Phase Project

Project Information and Objectives	Updated Update	18-Sep-18	Project Name	Al Montazah Waterpark Phase 2
	Client	SHARIAH INVESTMENT & DEVELOPMENT AUTHORITY	Construction Commencement Date	January 01, 2016
	Designer	Polin , Zampira	Construction Completion Date	15- Oct. 2018 (Green Park) , Soft Opening 28-October 2018
	Contractor	AL KHARAFI, ALBA TOWER, OHM ELECTROMECHANICAL LLC, RASHID AL OWAIS , AWW,ROCAS	Grand Opening Date	To Be finalized by Top Management
Project Financials		Project Overview		



Original Budget	98,000,000	
Updated Budget	135,000,000	
Signed Contract	107,832,537	
Variation Amount	27,808,531	
Total Paid	123,311,921	

The Project Concept is to enhance the experience of the existing water park in Al Montazah.

Components:

- Male / female changing rooms Restaurant , Cafee , Nurse room , Kids play area (Indoor and outdoor)
- Wave pool
- Multi- slides
- Theming concept
- The new target date to complete the development of water park on the 31st jan. 2018 , and the green park on 15th Oct. 2018 (Including Shifting the wheel)

Key Project Milestones

Milestone	Due Date	Status	Name	Impact	Status / Notes
Concept Design		Done	Al Muntazah Team	High	
Schematic Design		Done	Theming Contractor (ROCAS)	High	
Detailed Design		Done	Wheel works (Biscwice)	Medium	
Interior Design		Done	Zampira (Rides supplier)	High	
Construction Package		Done	Internal Processes		
Hording Installation & Artwork		N/A	Responsible Department	Task	Status
Authoritie approval		Approval obtained from SEWA for additional 500 KVA in water park	Marketing	To Coordinate with All Muntazah Team	
Construction works		On Going - Last stage (testing and Commissioning)	Public Relations	To Coordinate with All Muntazah Team	
Landscape		On going	Government Relations	N/A	
Lighting		On going (Flood Light and Theming light)	Procurement	All project related items are under control	
Public Furniture		By Al Muntazah	Legal	Legal issue against Khuraif	
CCTV		On Going	Business Development		
Sound System		On Going	IT Technical Support	Supply and installation of Turnstiles	To be done before 10 th October, 2018
FF&E		By Al Muntazah (To check furniture for Fat and Elevation Burger	Property Management	To Coordinate with All Muntazah Team	
OS&E		By Al Muntazah	Operation		
Kitchen equipments		By Al Muntazah	Finance	Some delays payment	Pushing to release it ASAP
Signages & Wayfinding		By Al Muntazah			
Fire System		Finalized recently			
SEWA /Authorities Connection		Approvals ottined , civil works on going			
Snagging		On Going for water park			
Handover		Not started			

* Please refer to the attached Action sheet filled by the concerned department

FOR Chairman's Attention

Description	Urgency	Status	Action	Impact	Indication	Mitigate
Legal case to be raised against M/S Kharaif		Ongoing	Operating the park without finalizing spare part agreement with Zampira	Any defect in any spare part will affect the operation of the ride as it was not available in stock		Revised quotation received from Zampira , and forwarded to Al Muntazah to finalize
Rocas agreement		Ongoing	Over Budgeting due new scope of works required			
Items Related to operation by Al Muntazah	High	On going	Delays in finalizing Kitchen Equipment in the Green Park			The installation contractor has been assigned
Delay of Rocas Works	High	On going	ROCAS Bad Quality of material supplied to site	Delay in project completion date		
			Rocas agreement not yet finalized	relasing the payment without contractual support		
			Operation items by al Muntazah (Reception Counter , Service agreement with BISSWIS , Kitchen Equipments)	Delay operation date		

Project to Capture Details of all Shurooq Projects. Specifications tab will be used to capture additional information



PMWeb 1 Search PMWeb... Power

(Portfolio) > Portfolio > Lists > Projects

Boston Medical Center

Program Commercial
Project ID* RVS0104
Name* Boston Medical Center
Location BLDG00A2 - Hospital
Project Status Completed
Project Type New Construction
Category -- Select --
Status Approved
Revision 0 Date
Request ID

Currency USD - Dollar (United States of America)
PBS (Portfolio)
Program WBS Select Program WBS
Target Budget \$0.00
Target Revenue \$0.00
Target Duration 0 UOM -- Select --
Target Start **Target Finish**
Percent Complete 0.00%
Scope

Image Gallery

Details Specifications Locations Phases WBS Users Companies Contacts Checklists (9) Payments Clauses Notes (2) Attachments (4)

Address

Address 1 1 Boston Medical Center Place
Address 2
City Boston
State MA Zip 02118
Country USA
Phone (617) 638-8000
Fax

Tags

Latitude 25.220884
Longitude 55.342566
Elevation
Google Address 1 Boston Medical Center PlaceBoston, MA

Personnel

Client Universal Corporation
GC W. Turner Construction
Architect / Engineer Wagner & Williams
Executive Steve Watson
Manager Dominique Pedrosa
Superintendent Mark Waters
Commitment Company W. Turner Construction
Owner Universal Corporation

Linked Assets

Suite	Location	Building	Floor	Space	Equipment
No records to display.					

Page Size 10

Cost Breakdown Structure








(Portfolio) > Cost Management > Budgets > Cost Codes








Boston GC




 Edit
  Refresh

Level #	Description*	# of Characters	Values
001	Division	2	
002	Detail	5	

Details
 Notes
 Attachments

Drag a column header and drop it here to group by that column

 Edit
  Add
  Delete
  Refresh
  Paste From Excel
  Export To Excel

Inactive ☐	Cost Code	Description	Division	Detail	Notes	Account
☐	01-01000	General Conditions	01 - General Conditions	01000 - General Conditions		
☐	01-01010	General Expenses	01 - General Conditions	01010 - General Expenses		
☐	01-01020	Project Staffing	01 - General Conditions	01020 - Project Staffing		
☐	01-01030	Field Offices	01 - General Conditions	01030 - Field Offices		
☐	01-01040	Temporary Utilities	01 - General Conditions	01040 - Temporary Utilities		
☐	01-01050	Safety & Protection	01 - General Conditions	01050 - Safety & Protection		
☐	01-01060	Cleaning	01 - General Conditions	01060 - Cleaning		
☐	01-01070	Miscellaneous Expense	01 - General Conditions	01070 - Miscellaneous Expense		
☐	01-01080	Labor, Insurance, & Taxes	01 - General Conditions	01080 - Labor, Insurance, & Taxes		
☐	01-01090	GLPD	01 - General Conditions	01090 - GLPD		
☐	01-01100	Winter Conditions	01 - General Conditions	01100 - Winter Conditions		
☐	01-01110	Testing & Inspections	01 - General Conditions	01110 - Testing & Inspections		
☐	01-01120	Hoisting	01 - General Conditions	01120 - Hoisting		
☐	02-02000	Sitework & Demolition	02 - Sitework & Demolition	02000 - Sitework & Demolition		
☐	02-02010	Subsurface Investigation	02 - Sitework & Demolition	02010 - Subsurface Investigation		
☐	02-02015	Asbestos & Lead Abatement	02 - Sitework & Demolition	02015 - Asbestos & Lead Abatement		
☐	02-02020	Demolition	02 - Sitework & Demolition	02020 - Demolition		
☐	02-02100	Site Preparation	02 - Sitework & Demolition	02100 - Site Preparation		

CMCS recommends that cost breakdown structure be aligned with the awarded contracts per project



010 All

020 Design Fee

030 Supervision Fee

040 Construction Contract

050 Provisional Sums

060 Contingency

Financial Periods



Search PMWeb...



(Portfolio) > Portfolio > Lists > Periods



Periods for Boston Medical Center

Edit Add Delete Refresh Generate Next

#	Period	Budget Year	From Date	To Date
1	Jan 11	2011	01-01-2011	01-31-2011
2	Feb 11		02-01-2011	02-28-2011
3	Mar 11		03-01-2011	03-31-2011
4	Apr 11		04-01-2011	04-30-2011
5	May 11		05-01-2011	05-31-2011
6	June 11		06-01-2011	06-30-2011
7	July 11		07-01-2011	07-31-2011
8	Aug 11		08-01-2011	08-31-2011
9	Sep 11		09-01-2011	09-30-2011
10	Oct 11		10-01-2011	10-31-2011
11	Nov 11		11-01-2011	11-30-2011
12	Dec 11		12-01-2011	12-31-2011
13	Jan 12		01-01-2012	01-31-2012
14	Feb 12		02-01-2012	02-29-2012
15	Mar 12		03-01-2012	03-31-2012
16	Apr 12		04-01-2012	04-30-2012
17	May 12		05-01-2012	05-31-2012

Database: Marc

User: Bassam Samman

Budget Module



1
Search PMWeb...
?

(Portfolio) > Cost Management > Budgets > Budgets

215 - Boston Medical Center - Construction Budget
?

Project* Boston Medical Center
Revision 2 Date 09-22-2011 Estimate
Status Approved Description Construction Budget


Details Adjustments Specifications Clauses Notes Attachments (1) Notifications

Drag a column header and drop it here to group by that column

Edit + + Add Cost Codes X Delete Update Tasks Refresh Paste From Excel Export To Excel WBS Levels... Use Units Layouts

Line #	Attachments	Cost Code*	Group1	Description	Contingency	Adjustment 1	Tax	Adjustment 2	Original Project Budget	Cost Type	Funding	Company	Task
001	(Q)	01-000001	01 - Land Costs	Land Acquisition	\$1,200,000.00	\$0.00	\$0.00	\$0.00	\$1,200,000.00		\$0.00		02 - Award F
002	(Q)	01-000002	01 - Land Costs	Land Permits and Fees	\$450,000.00	\$0.00	\$0.00	\$0.00	\$450,000.00		\$0.00		03 - Award S
003	(Q)	02-010002	02 - Hard Costs	General Conditions	\$197,500.00	\$0.00	\$0.00	\$0.00	\$197,500.00		\$0.00		06 - Clearing
004	(Q)	02-020000	02 - Hard Costs	Existing Conditions	\$1,100,000.00	\$0.00	\$0.00	\$0.00	\$1,100,000.00		\$0.00		08 - Prepare
005	(Q)	02-030000	02 - Hard Costs	Concrete	\$875,000.00	\$0.00	\$0.00	\$0.00	\$875,000.00		\$0.00		10 - Fabricat
006	(Q)	02-050000	02 - Hard Costs	Metals	\$850,000.00	\$0.00	\$0.00	\$0.00	\$850,000.00		\$0.00		11 - Prepare
007	(Q)	02-061000	02 - Hard Costs	Rough Carpentry	\$122,500.00	\$0.00	\$0.00	\$0.00	\$122,500.00		\$0.00		13 - Fabricat
008	(Q)	02-099000	02 - Hard Costs	Painting and Coating	\$300,000.00	\$0.00	\$0.00	\$0.00	\$300,000.00		\$0.00		15 - Layout f
009	(Q)	02-210000	02 - Hard Costs	Fire Suppression	\$450,000.00	\$0.00	\$0.00	\$0.00	\$450,000.00		\$0.00		16 - Excavate
010	(Q)	02-220000	02 - Hard Costs	Plumbing	\$415,000.00	\$0.00	\$0.00	\$0.00	\$415,000.00		\$0.00		30 - Rough f
011	(Q)	02-230000	02 - Hard Costs	HVAC	\$410,000.00	\$0.00	\$0.00	\$0.00	\$410,000.00		\$0.00		10 - Fabricat
012	(Q)	02-260000	02 - Hard Costs	Electrical	\$52,000,000.00	\$0.00	\$0.00	\$0.00	\$52,000,000.00		\$0.00		
013	(Q)	02-310000	02 - Hard Costs	Earthwork	\$530,000.00	\$0.00	\$0.00	\$0.00	\$530,000.00		\$0.00		
014	(Q)	03-003000	03 - Soft Costs	Design Architect	\$535,000.00	\$0.00	\$0.00	\$0.00	\$535,000.00		\$0.00		

Budget Projection

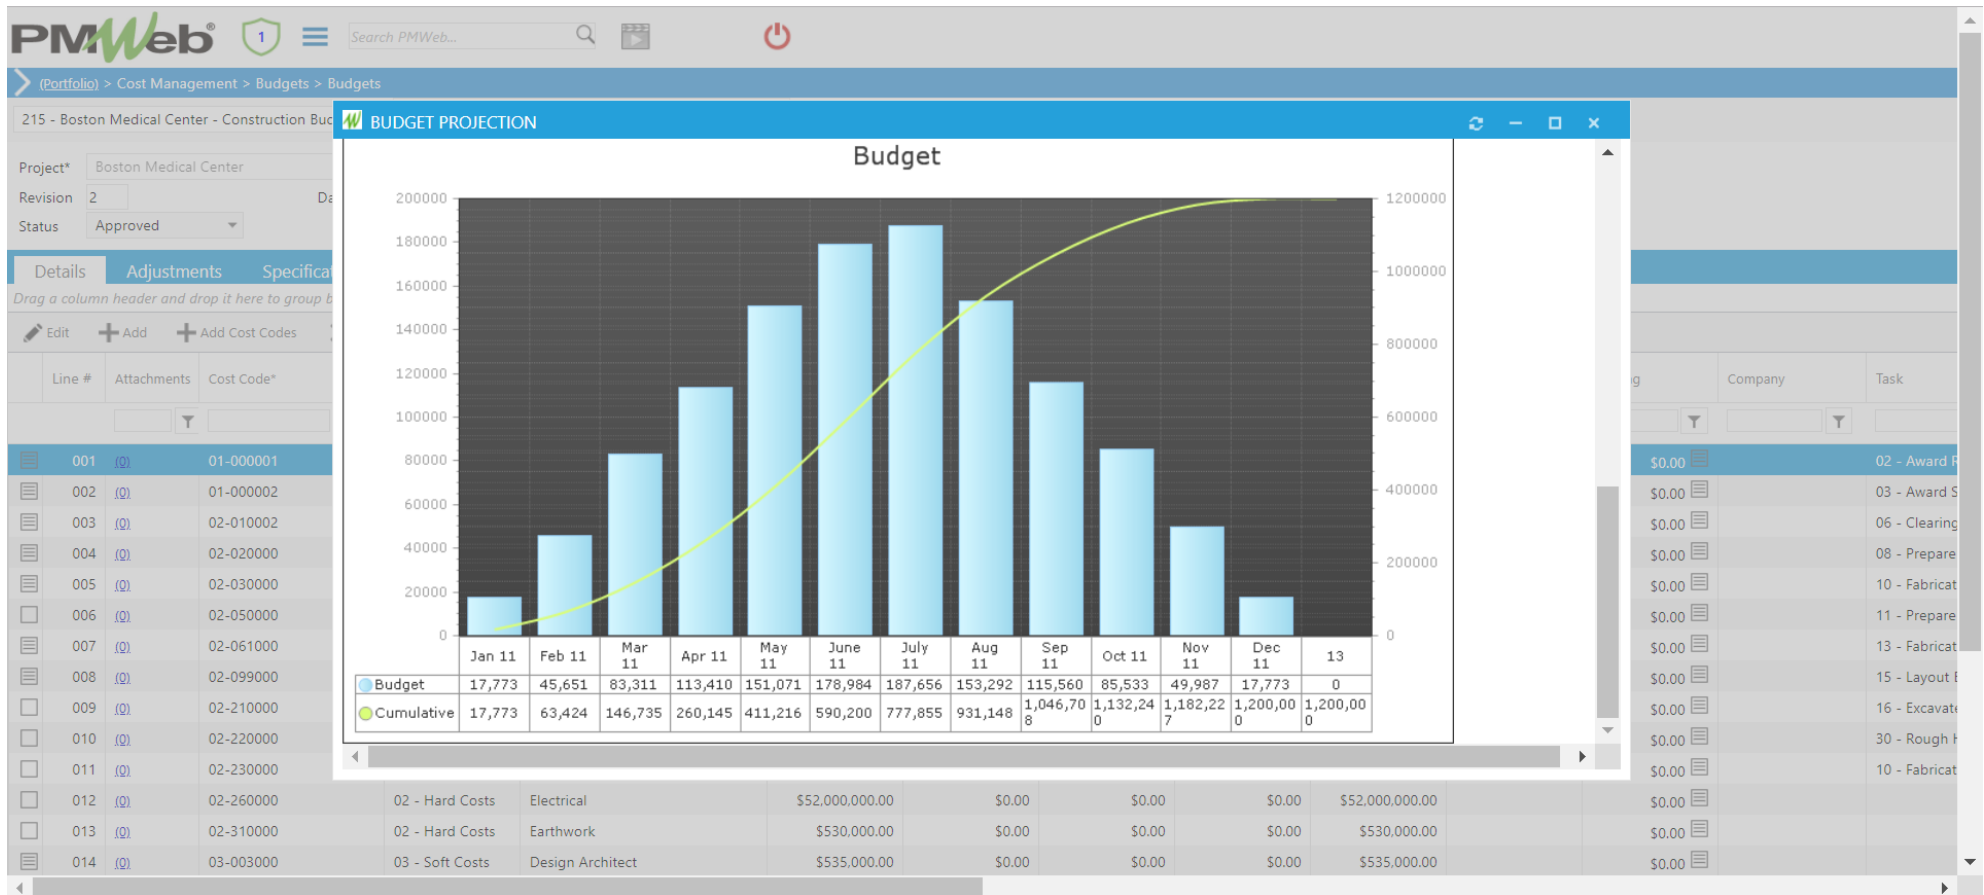

Budget Transfers and Adjustment

(Portfolio) > Cost Management > Budgets > Budget Requests

Boston Medical Center - 1 Budget Transfer      

Project* Reference

Record #* Category

Type

Description

Estimate

Status

Revision Date

Post As

DetailsAdjustmentsSpecificationsClausesNotesAttachments (2)Notifications

Drag a column header and drop it here to group by that column

EditAddAdd Cost CodesDeleteRefreshUse UnitsLayouts

	Line	Attachments	Cost Code*	Description	UOM	Quantity	Unit Cost	Adjustment 1	Tax	Adjustment 2	Project Bud	Cost Type	Funded	Unit Price	Owner Budget	Company
☐	001	(0)	02-030000	Concrete		1.00	\$50,000.00	\$0.00	\$0.00	\$0.00	\$50,000.00		\$0.00	\$50,000.00	\$50,000.00	
☐	002	(0)	05-005000	Project Contingenc		1.00	\$-50,000.00	\$0.00	\$0.00	\$0.00	\$-50,000.00		\$0.00	\$-50,000.00	\$-50,000.00	
						2.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00			\$0.00	\$0.00	

1

Page size: 20

Created: 09-27-2011 by admin - Admin

Budget Request Output Form



PROJECT DEPARTMENT / BUDGET REQUEST FORM (Request for Additional Budget for New Scope)		 شروق SHUROOQ	
Date		Ref. Number	
Project			
Location			
Original Budget			
Previously Approved Budget Variations			
New Scope of Work			
Details of Additional Scope/ Budget			
S.NO	Item Description	Total Approx.	
1			
2			
3			
4			
5			
6			
7			
TOTAL		AED	-
Total Amount for Requested Changes		Time Implementation on The project	
Revised Budgeted value after the Last Budget Request			
Attachments			
Original Contract Agreement (If Available)			
Supporting documents for the Requested Changes (Approved)			
Destination Request			
Destination Manager		COO	
Project Department			
Project Manager		Project Director	
CEO's Approval			
H.E. Marwan bin Jassim Al Sarkal			
Executive Chairman			

Commitment for Design, Supervision and Construction Contracts


1
Search PMWeb...
Power Icon

(Portfolio) > Cost Management > Contracts > Commitments

Boston Contractors - 002 - GMP Contract
Search
Print
Export
Generate...
?

Type: Subcontract
Project*: Boston Medical Center
ID*: 002
Company: Boston Contractors
Description: GMP Contract
Reference:
Category: -- Select --
Revision: 0
Status: Approved
Effective Date:
Days: 0.00
Procurement #:
Paid In Full: ☐

Billing
☒ Do not allow overbilling
☐ Allow overbilling
☐ Up to 0.00% % of revised value
☐ Up to 0.00% % of line item
Billing Terms: -- Select --
Retention on Services: 10.00%
Retention on Stored Materials: 10.00%
Delivery
Due Date: 09-23-2011
Scheduled Delivery Date: 09-23-2011
Ship Via: -- Select --
Ship To:

	Costs	Days
Original Value	\$4,800,000.00	0.00
Approved Changes	\$70,000.00	0.00
Revised Value	\$4,870,000.00	0.00
Billed	\$3,338,500.00	
Retained	\$333,850.00	
Balance Due	\$3,004,650.00	
Payments Applied	\$37,350.00	
Open Balance	\$2,967,300.00	
Unbilled	\$1,531,500.00	
Pending Changes	\$0.00	0.00
Projected Value	\$4,870,000.00	0.00

Details Adjustments Specifications Clauses (2) Change Orders Progress Invoices Payments Notes Attachments (30) Notifications

Drag a column header and drop it here to group by that column

Edit Add Items Add Delete Refresh Paste From Excel Export To Excel Use Units Layouts

	Line #	Attachments	Item	Description	UOM	Quantity	Unit Cost	Ext. Cost	Adjustment 1	Tax	Adjustment 2	Total Cost	Cost Type	Cost
☐	001	(0)		General Conditions		1.00	\$415,000.00	\$415,000.00	\$0.00	\$0.00	\$0.00	\$415,000.00		02-C
☐	002	(0)		Existing Conditions		0.09	\$1,000,000.00	\$90,000.00	\$0.00	\$0.00	\$0.00	\$90,000.00		02-C
☐	003	(0)		Concrete		1.00	\$850,000.00	\$850,000.00	\$0.00	\$0.00	\$0.00	\$850,000.00		02-C

Project Cost Report - BLANK



Project Name								
Budget								
Deadline								
		Contract Details						
Vendor	Scop of Work	Contract Value	Variation	Revised Contract Value	Invoice Amount	Payment Amount	Balance to Pay	Remarks
DESIGN								
CONSTRUCTION								
TOTAL		0.00		0.00	0.00	0.00	0.00	
Design Cost		-						
Construction Cost		0.00						
		-						

Project Cost Report to Show Details of All Commitments Within a Project



Project Name	Al Montazah Park Phase 2							
Budget	98,000,000.00 [98 M Closed Budget]							
Updated Budget	135,000,000.00							
Deadline	1-Jun-18							
	Contract Details							
Payments Thru	Vendor	Subject of Contract	Contract Value	Variation	BNW Contract Value	Invoice Amount	Paid Amount	Balance to pay
LC	Polo Water Park	Water Park Ride Installation	6,922,835.60		6,922,835.60	6,922,835.00	6,922,835.00	0.60
New LC &	Polo Water Park	New Water Slides Equipment	2,130,000.00	22,500.00	2,142,500.00	1,900,500.00	1,900,500.00	
LC	Antonio Zampola	Amusement Rides-1	12,331,000.00	-364,400.00	11,966,600.00	12,331,000.00	12,331,000.00	-364,400.00
LC	Zampola Asia Pacific	Amusement Rides-2	909,250.00	-25,450.00	883,800.00	909,800.00	948,800.00	-40,000.00
	Zampola Asia Pacific	New PO as Variations		37,684.40	37,684.40	37,684.40	37,684.40	0.00
Con	Suzidian Trading	Train Supplier	1,075,500.00		1,075,500.00	1,075,500.00	1,075,500.00	0.00
Shatoo	SAHMI	Consultancy	185,000.00		185,000.00	185,000.00	185,000.00	0.00
SRO	Rashid Al Odeh	Design and Supervision	720,000.00		720,000.00	720,000.00	720,000.00	0.00
Shatoo	Jack Ponce Associates	Master Plan	864,546.78		864,546.78	279,750.00	279,750.00	584,796.78
Shatoo	Polyester Threading Projects, S.L (Roca)	Concept Design (25 K Euro) & Detail Design (30K Euro)	176,800.00		176,800.00	176,800.00	176,800.00	0.00
SRO	Roca & Design	Threading (1 Gigan Amusement)	20,400,000.00	3,405,140.00	23,805,140.00	22,984,988.76	22,984,988.76	820,151.24
SRO	Al Kharaf Swimming Pools	Supply and Installation of Swimming Pools	2,000,000.00	805,200.00	2,805,200.00	1,761,990.00	1,671,990.00	633,210.00
SRO	Alba Tower Aluminum Factory Ltd.	Boarding Work	854,500.00		854,500.00	740,600.00	740,600.00	113,900.00
Shatoo/SRO	Alba Tower Aluminum Factory LLC	Cafes & Restaurants , Concrete foundations for rides	6,750,000.00	4,908,661.00	11,658,661.00	9,880,179.90	9,880,179.90	1,778,481.10
Shatoo/SRO	Alba Tower Aluminum Factory LLC	New Existing Building ,Changing Room and Male/Female Toilet, Two Pump Rooms & Kitchen & Nursery	3,200,000.00	5,208,200.00	8,408,200.00	7,558,470.00	7,558,470.00	849,730.00
SRO	Amusement White Water Ltd.	Threading for Water Park	12,750,000.00	-532,197.00	12,217,803.00	12,468,905.00	11,468,905.00	768,898.00
SRO	Masters Events Management (Psc)	Professional & Reliable Service	521,185.00	9,792,091.75	10,313,276.75	8,207,007.80	8,107,007.80	2,142,189.45
SRO	Interlink	Supply of Spining Routs	1,186,720.00		1,186,720.00	237,344.00	237,344.00	949,376.00
SRO	Adheer Al Isawera	AC System	1,000,000.00	1,071,100.00	2,071,100.00	975,070.00	975,070.00	1,096,030.00
SRO	Al Dhah Al Dall	Supply of Light Fittings	1,212,328.50	56,290.50	1,268,619.00	1,268,619.50	1,268,619.50	0.00
SRO	Al Dhah Al Dall	Supply of Light Fittings New PO	429,000.00		429,000.00	429,000.00	429,000.00	0.00
Shatoo-Boucy	Playlin SA	Supply/Installation of Playground Castel Concept	585,500.00	0.00	585,500.00	267,750.00	267,750.00	317,750.00
Shatoo SMS -cgrus	National Pest Control	Annual Pest Control Service	50,000.00	0.00	50,000.00			50,000.00
Shatoo	Al Rayyah Al Haditha Computer Ty	IP Camera & PA solution	1,054,417.00		1,054,417.00	1,249,041.00	1,249,041.00	-195,624.00
Shatoo	OHM Star Electronics LLC	Water & Infrastructure	2,800,000.00	3,524,000.00	6,324,000.00	5,607,765.00	5,607,765.00	716,235.00
Shatoo	ARD	Survey Crew on Daily Bids	280,000.00	245,400.00	525,400.00	437,820.00	437,820.00	47,580.00
Shatoo	ARD	Tree Survey	8,800.00		8,800.00	8,800.00	8,800.00	0.00
Shatoo	Feature Park	Removal of Palm Trees	10,000.00		10,000.00	10,000.00	10,000.00	0.00
Shatoo	Khamsheh Sykes LLC	De-watering	28,170.00		28,170.00	28,170.00	28,170.00	0.00
Shatoo-Boys	Extreme Adventures Group	Kids Play Equipment	878,580.00	47,250.00	725,750.00	321,000.00	321,000.00	404,750.00

Project Cost Report to Show Details of All Commitments Within a Project



	Wagner Bros	Luminaire servicing	348,400.00		348,400.00	348,400.00	348,400.00	0.00
Shamoo	Water Safety Product LLC	Supply of Life Jacket	210,362.62	0.00	210,362.62	210,362.62	210,362.62	0.00
Shamoo	Seminar Solution DMCC	Online Ticketing	1,602,604.60	147,661.00	1,680,304.60	1,523,375.70	1,523,375.70	156,928.90
Shamoo	Islaya Canada	Indoor Play Structure	2,643,372.50		2,643,372.50	817,309.00	817,309.00	1,826,063.50
Shamoo	Sanaoli	Winter Features (5 Nos.) + Existing Pool Maintenance	3,701,600.00		3,701,600.00	2,442,690.00	2,442,690.00	1,258,910.00
Shamoo	Al nahooda Interiors	Installation of Lockers	475,000.00		475,000.00	475,000.00	475,000.00	0.00
Shamoo	Jamar Flooring	Stamp Concrete For Water Park	2,600,000.00	-2,211,608.40	1,288,391.60	1,288,391.60	1,288,391.60	0.00
Shamoo	Jamar Flooring	Stamp Concrete For Green Park	2,600,000.00		2,600,000.00	1,665,000.00	1,665,000.00	935,000.00
Shamoo	Leisure Entertainment	Installation of Ribs	470,000.00		470,000.00	448,733.40	448,733.40	21,266.60
Shamoo	TSCC	Kitchen Equipments	671,600.00		671,600.00	479,672.00	479,672.00	191,928.00
Shamoo	Al Hala Mechanical & Office Equipments	Electrical supplies for the Cafeteria	14,000.00		14,000.00			14,000.00
Shamoo	Al Khaym Tents	63 m2 of Walk way shades	60,200.00		60,200.00	33,180.00	33,180.00	27,020.00
Shamoo	Shamoo Tents & Shades Industry	Steel enabling for indoor kids area	13,200.00		13,200.00	13,200.00	13,200.00	0.00
Shamoo	Genex	Supply of Chemicals	119,000.00		119,000.00			119,000.00
	SFMK	Support Service	9,713.00		9,713.00	9,713.00	9,713.00	0.00
New Proposed Business for new scope of work								
Shamoo	Qada Enter Phase	IP Network	710,336.00		710,336.00	674,837.25	674,837.25	35,498.75
Shamoo	Qada Enter Phase	CCTV	1,006,385.00		1,006,385.00	986,465.75	986,465.75	19,919.25
Shamoo	Sigma Technologies	IT Infrastructure	1,380,000.00		1,380,000.00	810,000.00	810,000.00	570,000.00
Shamoo	Shoraba AG	Marble Ramp	550,500.00	0.00	550,500.00	550,500.00	550,500.00	0.00
Shamoo	Shoraba AG	Relocation of Giant Wheel	1,818,082.91	186,682.91	1,818,082.91	1,818,082.91	1,818,082.91	0.00
Shamoo	Master Event	Relocation of Giant Wheel	1,150,000.00	0.00	1,150,000.00	1,150,000.00	1,150,000.00	0.00
Shamoo	Bright Link	Provision of Civil Work	1,305,362.50	1,670,112.00	3,325,688.30	2,371,509.70	2,371,509.70	954,178.60
Shamoo	Glisco	Foundation of Wheel	1,500,000.00	0.00	1,500,000.00	1,421,815.41	1,421,815.41	78,184.59
Shamoo	Redmi Al owaik	Design & Supervision	605,000.00	0.00	605,000.00	475,000.00	475,000.00	130,000.00
Shamoo	Al Shalukah	GRS Work	254,280.00	0.00	254,280.00	254,280.00	254,280.00	0.00
Shamoo	Rafico	Fire Fighting	600,000.00	47,250.00	647,250.00	207,250.00	207,250.00	440,000.00
Shamoo	Superior & Creative team	Civil Work	9,600.00	0.00	9,600.00	9,600.00	9,600.00	0.00
Shamoo	Gulf Fence Factory	Gate Link Fence	43,627.50	0.00	43,627.50	41,550.00	41,550.00	2,077.50
Shamoo	Sinco	Pool - Structure	63,200.00	26,800.00	111,700.00	41,600.00	41,600.00	70,100.00
Shamoo	Shadi General maintenance	Wave Pool Repair	31,500.00	0.00	31,500.00	31,500.00	31,500.00	0.00
Shamoo	Toronto Agriculture LLC	Supply of Plants	203,203.00	0.00	203,203.00	203,203.00	203,203.00	0.00
Shamoo	SCS Middle East	Ride Inspection	140,000.00	0.00	140,000.00	66,150.00	66,150.00	73,850.00
Shamoo	PMMA	Compressed Air Network	33,500.00	0.00	33,500.00	33,500.00	33,500.00	0.00
Shamoo	AMTC	Kitchen Equipments	105,000.00	0.00	105,000.00	40,000.00	40,000.00	65,000.00
Shamoo	Mehdi Al Tagh	LED Light	8,960.00	0.00	8,960.00	8,960.00	8,960.00	0.00
Shamoo	Technopol	8m HDS Tubular Pole	65,360.00	0.00	65,360.00	65,360.00	65,360.00	0.00
Shamoo	Green Horticulture	Supply of pots	9,480.00	0.00	9,480.00	9,480.00	9,480.00	0.00
Shamoo	Fawa Ref. & APC Co	Servicing window AC	5,590.00	0.00	5,590.00	5,590.00	5,590.00	0.00
			107,644,787.30	27,808,530.96	135,453,318.26	119,220,177.46	119,150,907.46	16,299,410.80

Change Order Request



Search PMWeb...



(Portfolio) > Cost Management > Change Management > Online Change Requests

001 - Boston Medical Center -



Company: Boston Contractors
Project*: Boston Medical Center
Commitment*: 002 - GMP Contract
Description:
Reference:
Record #*: 001
Status: Approved Revision: 0
Change Event:
Risk Analysis: 1 - Test
Commitment Change Order:

Requested
Request Date: 10-19-2016
Needed By:
Cause: -- Select --
Contact:
Comment:
Submit

Change Request Recap
Costs Days
Original Value \$4,800,000.00 0.00
Approved Changes \$70,000.00 0.00
Revised Value \$4,870,000.00 0.00
This Request \$13.50 0.00
Type: -- Select --
Category: -- Select --
Post As: Revised Scope

Details Specifications Notes Attachments

Drag a column header and drop it here to group by that column

Line #	Attachments	Description	Item	UOM	Quantity	Unit Cost	Ext. Cost	Cost Code	Cost Type	Days	Phase	WBS	Period
001	(0)	10- Asbestos Removal Allowance	5726		1.00	\$0.00	\$0.00			0.00			
002	(0)	10- Formwork	5839	Is	1.00	\$0.00	\$0.00			0.00			
003	(0)	120- Form Supported Beams	5850	sfca	1.00	\$10.00	\$10.00			0.00			
004	(0)	30- Form Column Footing	5841	sfca	1.00	\$3.50	\$3.50			0.00			
					4.00	\$13.50	\$13.50			0.00			

Page Size: 20

Created: 10-19-2016 by admin - Admin

Change Order Request Output Form



PROJECT DEPARTMENT / CHANGE ORDER REQUEST FOR SHUROOO				
Date		Ref. Number		
Project				
Location				
Budget				
Scope of Work				
Reasons of Change Request				
To Be Filled by the Concerned Consultants				
Details of Requested Changes				
S.NO	Item Description	Quantity	Rate	Total
Total Amount for Requested Changes		Time Implementation on The project		
Attachments				
Original Contract Agreement (If Available)				
Supporting documents for the Requested Changes (Approve				
Approvals				
Construction Dept.		Project Dept.	Head of the Project	
Name & Signature		Name & Signature	Name & Signature	

Variation Orders



PMWeb®

1

≡

Search PMWeb...

🔍

📅

🔌

(Portfolio) > Cost Management > Change Management > Commitment COs

001 - Boston Medical Center - Office Modifications 🔍 📄 🗑️ 📁 📧 🖨️ ?

Project*

Boston Medical Center

Commitment*

002 - Boston Contractors - GMP Contract

Company

Boston Contractors

Type

Subcontract

Record #*

001

Description

Office Modifications

Post As

Revised Scope

Revision

0

Date

09-27-2011

Status

Approved

Change Request

Select Change Request...

Cause

-- Select --

Requested By

Select Company

Category

-- Select --

Reference

Assigned To

Select Company

Change Order Date

Effective Date

Days

0.00

Recap

		Days
Original Commitment Amount	\$4,800,000.00	0.00
Prior Approved Changes	\$0.00	0.00
Prior Revised Contract	\$4,800,000.00	0.00
Total of This Change	\$70,000.00	0.00
Contract to This Change	\$4,870,000.00	0.00

Details Adjustments Specifications Clauses Notes Attachments (2) Notifications

Drag a column header and drop it here to group by that column

🔗 Link CE

🔗 Link Change Request(s)

➕ Add

📄 Add Items

✎ Edit

✖ Delete

🔄 Refresh

📏 Use Units

🏠 Layouts

⏪

1

⏩

Page Size

20

Created: 09-27-2011 by admin - Admin

Variation Order Output Form



PROJECT DEPARTMENT / VARIATION ORDER FORM				
				
Date		Ref. Number		
Project				
Location				
Contractor Name				
Contractor Name (If Available)		Original Contract Value(If Available)		
Budget				
Scope of Work				
Details of Requested Variation				
S.NO	Item Discription	Quantity	Rate	Total
1				
Total Amount for Claimed Variation				0.00
0.00				
Attachments				
Original Contract Agreement (If Available)				
Supporting documents for the claimed Variation (Approved)				
Change Order request (If Available)				
Approvals				
Construction Dept.			Project Dept.	
Name & Signature			Name & Signature	

Progress Invoices

PMWeb®



1

Search PMWeb...



(Portfolio) > Cost Management > Invoices > Progress Invoices

002 - Boston Medical Center - Boston Contractors -

Project* Boston Medical Center

Commitment* 002 - GMP Contract

Company Boston Contractors

Description Progress Invoice #6

Reference

Invoice # 8 [Create Next](#)

Record #* 8

Revision 0 Date 04-11-2016

Status Draft

Cost Period -- Select --

Category -- Select --

Paid In Full ☐

Online Invoice

Invoice Date 04-11-2016

Billing Terms -- Select --

Invoice Due

Invoice Type -- Select --

Contact

Comment

[Print Lien Waiver](#) ☐ Signed Lien Waiver attached

Contract Snapshot	
Original Value	\$4,800,000.00
Approved Changes	\$70,000.00
Revised Value	\$4,870,000.00
Invoiced	\$3,338,500.00
Retained	\$333,850.00
Earned Less Retainage	\$3,004,650.00
Less Prior Invoices	\$2,661,525.00
Current Payment Due	\$343,125.00
Unapplied Payments Available	\$0.00
Payments Applied	\$0.00
Open Balance	\$343,125.00
Bal. To Finish(incl. Retainage)	\$1,865,350.00

Details Adjustments Specifications Checklists (11) Payments Clauses Notes Attachments Workflow Notifications														
Drag a column header and drop it here to group by that column														
Edit	Delete	Refresh	Link Change Orders	% Complete From Schedule	Production	Use Units	Layouts							
Line #	Attachments	Cost Code	Description	UOM	Adjustment 1	Tax	Adjustment 2	Scheduled Quantity	Current Quantity	Prior Quantity	Unit Cost	Total Quantity	Scheduled Value	Pri Me
001	(0)	02-010002	General Conditions		\$0.00	\$0.00	\$0.00	1	0.00	0.55	\$415,000.00	0.55	\$415,000.00	
002	(0)	02-020000	Existing Conditions		\$0.00	\$0.00	\$0.00	1	0.00	0.90	\$1,000,000.00	0.90	\$1,000,000.00	
003	(0)	02-030000	Construction		\$0.00	\$0.00	\$0.00	1	0.00	0.00	\$850,000.00	0.00	\$850,000.00	

Actual Payment



PMWeb 1 Search PMWeb... Power

> (Portfolio) > Cost Management > Invoices > Progress Invoices US BR FR DE ES

002 - Boston Medical Center - Boston Contractors - Search Print Close Cancel Help

Project*
Boston Medical Center

Commitment*
002 - GMP Contract

Company
Boston Contractors

Description
Progress Invoice #6

Reference

Invoice #
8 Create Next

Record #*
8

Revision
0 Date 04-11-2016

Status
Draft

Cost Period
-- Select --

Category
-- Select --

Paid In Full
☐

Online Invoice

Invoice Date
04-11-2016

Billing Terms
-- Select --

Invoice Due

Invoice Type
-- Select --

Contact

Comment

Print Lien Waiver ☐ Signed Lien Waiver attached

Contract Snapshot

Original Value	\$4,800,000.00
Approved Changes	\$70,000.00
Revised Value	\$4,870,000.00
Invoiced	\$3,338,500.00
Retained	\$333,850.00
Earned Less Retainage	\$3,004,650.00
Less Prior Invoices	\$2,661,525.00
Current Payment Due	\$343,125.00
Unapplied Payments Available	\$0.00
Payments Applied	\$0.00
Open Balance	\$343,125.00
Bal. To Finish(incl. Retainage)	\$1,865,350.00

Details Adjustments Specifications Checklists (11) **Payments** Clauses Notes Attachments Workflow Notifications

Drag a column header and drop it here to group by that column

+ Add \$ Apply Payments Refresh Layouts

ID	Status	Company	Description	Payment Method	Payment #	Payment Date	Payment Amount	Cost Code	Period	Type	Category	Reference	Notes	Ap

No records to display.

\$0.00

1 Page Size 20

Created: 04-11-2016 by admin - Admin Database: Marc User: Bassam Samman

Bill Verification Report/ Progress Invoices Report



PROJECT DEPT / BILL VERIFICATION FORM						 شُرُوق SHUROOQ	
Project Name							
Scope of Work							
Contractor Name							
Agreed Contract Value			Contract Ref.				
Variation 01							
Variation 02							
Revised Contract Value	-						
Payment Terms							
Current Invoice Details							
Invoice Ref.	Invoice Date	Certified Amount	Certified Amount Including VAT	Certified Date	Remarks	Payment Status	
Previously Certified Payment Details							
Invoice Ref.	Invoice Date	Certified Amount	Certified Amount Including VAT	Certified Date	Remarks	Payment Status	
Total Certified(Previously)		-					
Grant Total		-					
Bill Certified By							
	Site Manager	Project Manager	Distination Manager	Finance	Received By(Account)		
Signature:							
Date:							
CEO's Approval							
H.E. Marwan bin Jassim Al Sarkal							
Executive Chairman							

Project Dashboard

Milestone Status




Construction Phase Project

Project Information and Objectives	Updated Update	18-Sep-18	Project Name	Al Montazah Waterpark Phase 2
	Client	SHARJAH INVESTMENT & DEVELOPMENT AUTHORITY	Construction Commencement Date	January 01, 2016
	Designer	Polin , Zampreia	Construction Completion Date	15- Oct. 2018 (Green Park) , Soft Opening 28-October 2018
	Contractor	AL KHARAFI, ALBA TOWER, OHM ELECTROMECHANICAL LLC, RASHID AL OWAIS , AWW,ROCAS	Grand Opening Date	To Be finalized by Top Management
Project Financials		Project Overview		



Cost sheet updates

Original Budget	98,000,000
Updated Budget	135,000,000
Signed Contract	107,832,537
Variation Amount	27,808,531
Total Paid	123,311,921



The Project Concept is to enhance the experience of the existing water park in Al Montazah.

Components:

- Male / female changing rooms Restaurant , Cafee , Nurse room , Kids play area (Indoor and outdoor)
- Wave pool
- Multi- slides
- Theming concept

- The new target date to complete the development of water park on the 31st Jan. 2018 , and the green park on 15th Oct. 2018 (Including Shifting the wheel)

Milestone	Due Date	Status
Concept Design		Done
Schematic Design		Done
Detailed Design		Done
Interior Design		Done
Construction Package		Done
Hording Installation & Artwork		N/A
Authority approval		Approval obtained from SEWA for additional 500 KVA in water park
Construction works		On going - Last stage (testing and Commissioning)
Landscape		On going
Lighting		On going (Flood Light and Theming light)
Public Furniture		By Al Montazah
OCTV		On going
Sound System		On going
FF&E		By Al Montazah (To check furniture for Fat and Elevation Burger
OS&E		By Al Montazah
Kitchen equipments		By Al Montazah
Signages & Wayfinding		By Al Montazah
Fire System		Finalized recently
SEWA /Authorities Connection		Approvals ottined , civil works on going
Snagging		On going for water park
Handover		Not started

Stakeholders List		
Name	Impact	Status / Notes
Al Montazah Team	High	
Theming Contractor (ROCAS)	High	
Wheel works (Biscowice)	Medium	
Amperia (Rides supplier)	High	
Internal Processes		
Responsible Department	Task	Status
Marketing	To Coordinate with All Montazah Team	
Public Relations	To Coordinate with All Montazah Team	
Government Relations	N/A	
Procurement	All project related items are under control	
Legal	Legal issue against Khuraif	
Business Development		
IT Technical Support	Supply and installation of Turnstiles	To be done before 10 th October, 2018
Property Management	To Coordinate with All Montazah Team	
Operation		
Finance	Some delays payment	Pushing to release it ASAP
* Please refer to the attached Action sheet filled by the concerned department		

Description	Urgency	Status	Action	Impact	Indication	Mitigate
Legal case to be raised against M/S Kharaif		Ongoing	Operating the park without finalizing spare part agreement with 'Zampreia	Any defect in any spare part will affect the operation of the ride as it was not available in stock		Revised quotation received from 'Zampreia , and forwarded to Al Montazah to finalize
Rocas agreement		Ongoing	Over Budgeting due new scope of works required			
Items Related to operation by Al Montazah	High	On going	Delays in finalizing Kitchen Equipment in the Green Park			The installation contractor has been assigned
Delay of Rocas Works	High	On going	ROCAS Bad Quality of material supplied to site	Delay in project completion date		
			Rocas agreement not yet finalized	relasing the payment without contractual support		
			Operation items by al Montazah (Reception Counter , Service agreement with BISSWISS , Kitchen Equipment's)	Delay operation date		

Custom Form To Report On Milestone Dates

		Project Milestones				
Executive Summary						
Design continues with Primary Infrastructure, BOH and Main Entry Facility submissions completed in June. The 60% DD Show Design for the entire park will be submitted from Riva by mid-July, which will be the bases of the park wide show procurement efforts. Site grading works to be complete in July and Phase I Infrastructure Utilities targeted to start by mid-July. The Theater substructure works targeted to be complete by the end of July 2014 and superstructure works commencing in August.						
Key Delivery Milestone Status						
#	Item	Target	Actual	Status		Comments
1	Theatre - Building Envelope Closeout	31 Dec 2014	08 Jan 2015	→	-6	
2	Start Foundation Works (Entry Plaza)	04 Aug 2014	25 Aug 2014	→	-21	Delays will be mitigated during construction. Not critical
3	Design Completion for Package B	30 Sep 2014	09 Oct 2014	→	-9	Not critical, as early package will be issued for procurement
4	Design Completion by Riva Arch	15 Oct 2014	15 Oct 2014	↓	0	
5	Project Completion & Handover	31 Mar 2016	31 Mar 2016	↓	0	
6	Theatre - Start Construction Works	01 Apr 2014	01 Apr 2014	↓	0	
7	Theatre - Start Steel Erection	11 Aug 2014	14 Aug 2014	→	-3	
8	Theatre - Completion & Handover	30 Sep 2014	30 Sep 2014	↓	0	
9	Placement of All Ride Orders	29 May 2014	05 Aug 2014	→	-68	
10	Design Completion by Riva Creative	29 Oct 2014	29 Oct 2014	↓	0	

Project Dashboard Stakeholders



Construction Phase Project

Updated Update

18-Sep-18

Client

SHARJAH INVESTMENT & DEVELOPMENT AUTHORITY

Designer

Polin , Zampreia

Contractor

AL KHARAFI, ALBA TOWER, OHM ELECTROMECHANICAL LLC, RASHID AL OWAIS , AWW,ROCAS

Project Information and Objectives

Project Name

Al Montazah Waterpark Phase 2

Construction Commencement Date

January 01,2016

Construction Completion Date

15- Oct. 2018 (Green Park) , 8th Opening 28-October 2018

Grand Opening Date

To Be finalized by Top Management

Project Overview

Project Financials

Cost sheet updates

Original Budget

98,000,000

Updated Budget

135,000,000

Signed Contract

107,832,537

Variation Amount

27,808,531

Total Paid

123,311,921

140,000,000

120,000,000

100,000,000

80,000,000

60,000,000

40,000,000

20,000,000

0

Signed Contract

Variation Amount

Total Paid

The Project Concept is to enhance the experience of the existing water park in Al Montazah.

Components:

- Male / female changing rooms Restaurant , Cafee , Nurse room , Kids play area (Indoor and outdoor)

- Wave pool

- Multi- slides

- Theming concept

- The new target date to complete the development of water park on the 31st jan. 2018 , and the green park on 15thOct.2018 (Including Shifting the wheel)

Key Project Milestones

Milestone

Due Date

Status

Concept Design

Done

Schematic Design

Done

Detailed Design

Done

Interior Design

Done

Construction Package

Done

Hording Installation & Artwork

N/A

Authority approval

Approval obtained from SEWA for additional 500 KVA in water park

Construction works

On going - Last stage (testing and Commissioning)

Landscape

On going

Lighting

On going (Flood Light and Theming light)

Public Furniture

By Al Montazah

CCTV

On going

Sound System

On going

FF&E

By Al Montazah (To check furniture for Fat and Elevation Burger

OS&E

By Al Montazah

Kitchen equipments

By Al Montazah

Signages & Wayfinding

By Al Montazah

Fire System

Finalized recently

SEWA /Authorities Connection

Approvals otted , civil works on going

Snagging

On Going for water park

Handover

Not started

Stakeholders List

Name

Impact

Status / Notes

Al Montazah Team

High

Theming Contractor (ROCAS)

High

Wheel works (Biscovic)

Medium

Zampreia (Rides supplier)

High

Internal Processes

Marketing

To Coordinate with All Montazah Team

Public Relations

To Coordinate with All Montazah Team

Government Relations

N/A

Procurement

All project related items are under control

Legal

Legal issue against Khuraif

Business Development

IT Technical Support

Supply and installation of Turnstiles

To be done before 10th October, 2018

Property Management

To Coordinate with All Montazah Team

Operation

Finance

Some delays payment

Pushing to releas it ASAP

* Please refer to the attached Action sheet filled by the concerned department

FOR Chairman's Attention

Description

Urgenoy

Status

Action

Impact

Indoation

Mitigate

Legal case to be raised against M/S Kharaif

Ongoing

Operating the park without finalizing spare part agreement with Zampreia

Any defect in any spare part will affect the operation of the ride as it was not available in stock

Revised quotation received from Zampreia , and forwarded to Al Montazah to finalize

Rocas agreement

Ongoing

Over Budgeting due new scope of works required

Items Related to operation by Al Montazah

High

On going

Delays in finalizing Kitchen Equipment in the Green Park

The installation contractor has been assigned

Delay of Rocas Works

High

On going

ROCAS Bad Quality of material supplied to site

Delay in project completion date

Rocas agreement not yet finalized

relasing the payemmnt without contractual support

Operation items by al Montazah (Reception Counter , Service agreement with BISSWISS , Kitchen Equipments)

Delay operation date

شركة الاستثمار والتنمية
SHARJAH INVESTMENT AND
DEVELOPMENT AUTHORITY

شروق
SHUROOQ



 Edit  Add  Delete  Refresh											
Stakeholder Name	Contact Person	Current Influence	Current Impact	Desired Influence	Desired Impact	What is important to the stakeholder	How could stakeholder contribute to the project	How could stakeholder block the project	Strategy for engaging the stakeholder	Managed by Company	Managed by Contact
Langdon Wilson	Fausto Martinez (	4	3	3	5	Schedule	Ontime paymen	Delay Payment	Quarterly Meetii	Jeddah Economic	Mounib Hammou







 Page Size

Project Dashboard

Actions By Department



Construction Phase Project							
Project Information and Objectives	Updated Update	18-Sep-18		Project Name	Al Montazah Waterpark Phase 2		
	Client	SHARJAH INVESTMENT & DEVELOPMENT AUTHORITY		Construction Commencement Date	January 01,2016		
	Designer	Polin , Zampreia		Construction Completion Date	15- Oct. 2018 (Green Park) , Soft Opening 28-October 2018		
	Contractor	AL KHARAFI, ALBA TOWER, OHM ELECTROMECHANICAL LLC, RASHID AL OWAIS , AIWW,ROCAS		Grand Opening Date	To Be finalized by Top Management		
Project Financials				Project Overview			
Cost sheet updates							
Original Budget	98,000,000			The Project Concept is to enhance the experience of the existing water park in Al Montazah.			
Updated Budget	135,000,000			Components:			
Signed Contract	107,832,537			- Male / female changing rooms Restaurant , Cafee , Nurse room , Kids play area (Indoor and outdoor)			
Variation Amount	27,808,531			- Wave pool			
Total Paid	123,311,921			- Multi- slides			
				- Theming concept			
				- The new target date to complete the development of water park on the 31st jan. 2018 , and the green park on 15 th Oct.2018 (Including Shifting the wheel)			
Key Project Milestones				Stakeholders List			
Milestone	Due Date	Status		Name	Impact	Status / Notes	
Concept Design		Done		Al Muntazah Team	High		
Schematic Design		Done		Theming Contractor (ROCAS)	High		
Detailed Design		Done		Wheelworks (Bioswim)	Medium		
Interior Design		Done		Zampreia (Ride supplier)	High		
Construction Package		Done		Internal Processes:			
Hording Installation & Artwork		N/A		Responsible Department	Task	Status	
Authority approval		Approval obtained from SEWA for additional 500 KVA in water park		Marketing	To Coordinate with All Muntazah Team		
Construction works		On Going - Last stage (testing and Commissioning)		Public Relations	To Coordinate with All Muntazah Team		
Landscape		On going		Government Relations	N/A		
Lighting		On going (Flood Light and Theming light)		Procurement	All project related items are under control		
Public Furniture		By Al Muntazah		Legal	Legal issue against Khuraif		
CCTV		On Going		Business Development			
Sound System		On Going		IT Technical Support	Supply and installation of Turnstiles	To be done before 10 th October, 2018	
FF&E		By Al Muntazah (To check furniture for Fat and Elevation Burger		Property Management	To Coordinate with All Muntazah Team		
OS&E		By Al Muntazah		Operation			
Kitchen equipments		By Al Muntazah		Finance	Some delays payment	Pushing to releas it ASAP	
Signages & Wayfinding		By Al Muntazah					
Fire System		Finalized recently					
SEWA /Authorities Connection		Approvals ottined , civil works on going					
Snagging		On Going for water park					
Handover		Not started					
				* Please refer to the attached Action sheet filled by the concerned department			
FOR Chairman's Attention				Risk			
Description	Urgency	Status		Action	Impact	Indication Mitigate	
Legal case to be raised against M/S Kharaif		Ongoing		Operating the park without finalizing spare part agreement with Zampreia	Any defect in any spare part will affect the operation of the ride as it was not available in stock	 Revised quotation received from Zampreia , and forwarded to Al Muntazah to finalize	
Rocas agreement		Ongoing		Over Budgeting due new scope of works required			
Items Related to operation by Al Muntazah	High	On going		Delays in finalizing Kitchen Equipment in the Green Park		 The installation contractor has been assigned	
Delay of Rocas Works	High	On going		ROCAS Bad Quality of material supplied to site	Delay in project completion date		
				Rocas agreement not yet finalized	relasing the payemnt without contractual support		
				Operation items by al Muntazah (Reception Counter , Service agreement with BIS&WIS , Kitchen Equipment's)	Delay operation date		

Actions By Department where they can details steps completed by them



PMWeb 1 ≡ 🔍 📄 🔌

(Portfolio) > Engineering Forms > Action Items 🇺🇸 🇧🇷 🇫🇷 🇩🇪 🇪🇸 🇮🇹 🇨🇳

Boston Medical Center - 001 - Issues raised by board 🔍 📄 📁 📧 🖨 🔄 Generate... 👤 Assign ?

Project* Boston Medical Center User Bassam Samman
 Phase -- Select -- WBS A - Planning and Design
 Action Item #* 001 CSI Code
 Description Issues raised by board members about Category Startup
 Status Draft Reference
 Revision 0 Date 03-28-2017 Priority High

Transmittals
 Date To Via
 No records to display.
 ⏪ ⏩ 1 Page Size 5

Details Specifications Checklists Clauses Notes Attachments (6) Collaborate Notifications

Drag a column header and drop it here to group by that column

✏ Edit ➕ Add 🔄 Refresh ✖ Delete 📄 Layouts

Line #	Attachments	Description	Assigned To	Due	Notes	Completed	Done
00001	📎	Action Step No. 1	JFK Finishes - Alex Franklin	05-07-2017		08-08-2018	☒
00002	📎	Action Step No. 2	Rockwell Architects - Ann Rockwell	05-09-2017			☐
00003	📎	Action Step No. 3	Rocker's Drywall - Rob Malone	05-10-2017			☐
00004	📎	Action Step No. 4	Boland Brothers - Will Walker	05-12-2017			☐
00005	📎	Action Step No. 5	Miami HVAC - starsky	05-14-2017			☐
00006	📎	Action Step No. 6	Timberland Management - Steve Prentiss	05-16-2017			☐
00007	📎	Action Step No. 7	Wagner & Williams - Karen Watson	05-16-2017			☐

⏪ ⏩ 1 Page Size 20

Linked Records

🔗 Add Link 🔄 Refresh ✖ Delete Link

Description	Rev.	Date	Type
-------------	------	------	------

Project Dashboard Issues




Construction Phase Project

Project Information and Objectives	Updated Update	18-Sep-18	Project Name	Al Montazah Waterpark Phase 2
	Client	SHARJAH INVESTMENT & DEVELOPMENT AUTHORITY	Construction Commencement Date	January 01, 2016
	Designer	Polin , Zampreia	Construction Completion Date	15- Oct. 2018 (Green Park) , Soft Opening 28-October 2018
	Contractor	AL KHARAFI, ALBA TOWER, OHM ELECTROMECHANICAL LLC, RASHID AL OWAIS , AWW,ROCAS	Grand Opening Date	To Be finalized by Top Management
Project Financials		Project Overview		



Cost sheet updates

Original Budget	98,000,000
Updated Budget	135,000,000
Signed Contract	107,832,537
Variation Amount	27,808,531
Total Paid	123,311,921



The Project Concept is to enhance the experience of the existing water park in Al Montazah.

Components:

- Male / female changing rooms Restaurant , Cafee , Nurse room , Kids play area (Indoor and outdoor)
- Wave pool
- Multi- slides
- Theming concept
- The new target date to complete the development of water park on the 31st jan. 2018 , and the green park on 15th Oct. 2018 (Including Shifting the wheel)

Key Project Milestones

Milestone	Due Date	Status
Concept Design		Done
Schematic Design		Done
Detailed Design		Done
Interior Design		Done
Construction Package		Done
Harding Installation & Artwork		N/A
Authoritie approval		Approval obtained from SEWA for additional 500 KVA in water park
Construction works		On going - Last stage (testing and Commissioning)
Landscape		On going
Lighting		On going (Flood Light and Theming light)
Public Furniture		By Al Montazah
CCTV		On Going
Sound System		On Going
FF&E		By Al Montazah (To check furniture for Fat and Elevation Burger
OS&E		By Al Montazah
Kitchen equipments		By Al Montazah
Signages & Wayfinding		By Al Montazah
Fire System		Finalized recently
SEWA /Authorities Connection		Approvals obtined , civil works on going
Snagging		On Going for water park

Stakeholders List

Name	Impact	Status / Notes
Al Montazah Team	High	
Theming Contractor (ROCAS)	High	
Wheel works (Biscowice)	Medium	
Zampreia (Rides supplier)	High	
Internal Processes		
Responsible Department	Task	Status
Marketing	To Coordinate with All Montazah Team	
Public Relations	To Coordinate with All Montazah Team	
Government Relations	N/A	
Procurement	All project related items are under control	
Legal	Legal issue against Kharaft	
Business Development		
IT Technical Support	Supply and installation of Turnstiles	To be done before 10 th October, 2018
Property Management	To Coordinate with All Montazah Team	
Operation		
Finance	Some delays payment	Pushing to release it ASAP

* Please refer to the attached Action sheet filled by the concerned department

FOR Chairman's Attention

Description	Urgency	Status
Legal case to be raised against M/S Kharaft		Ongoing
Rocas agreement		Ongoing
Items Related to operation by Al Montazah	High	On going
Delay of Rocas Works	High	On going

Issue	Impact	Indication	Mitigate
operating the park without finalizing spare part agreement with Zampreia	Any defect in any spare part will affect the operation of the ride as it was not available in stock		Revised quotation received from Zampreia , and forwarded to Al Montazah to finalize
Over Budgeting due new scope of works required			
Delays in finalizing Kitchen Equipment in the Green Park			The installation contractor has been assigned
ROCAS Bad Quality of material supplied to site	Delay in project completion date		
Rocas agreement not yet finalized	releasing the payment without contractual support		
operation items by al Montazah (Reception Counter , Service agreement with BISSWISS , Kitchen Equipment's)	Delay operation date		

Issue Resolution Custom Form

Details
Notes
Attachments



Issue Resolution Form

Project :	Mir-CMCSPrac	Date :	01-23-2017
Project Manager :	Syed Ali Hasan (Collabc	Status :	Draft
Issue ID :	1	Risk ID :	1
Raised By :	Ahmed Ghazy (Collabo	Raised Date :	01-23-2017
Issue Description : Description Text.			
Issue Impact : Impact Text.			
Recommended Action for Issue Resolution : Action for resolution of the risk.			

Note : The Risk ID will be the Record No. from the respective Risk Assessment.

Project Dashboard Risks




Construction Phase Project

Project Information and Objectives	Updated Update	18-Sep-18	Project Name	Al Montazah Waterpark Phase 2
	Client	SHARJAH INVESTMENT & DEVELOPMENT AUTHORITY	Construction Commencement Date	January 01, 2016
	Designer	Polin , Zampreia	Construction Completion Date	15- Oct. 2018 (Green Park) , Soft Opening 28-October 2018
	Contractor	AL KHARAFI, ALBA TOWER, OHM ELECTROMECHANICAL LLC, RASHID AL OWAIS , AWW,ROCAS	Grand Opening Date	To Be finalized by Top Management
Project Financials		Project Overview		



Cost sheet updates

Original Budget	98,000,000
Updated Budget	135,000,000
Signed Contract	107,832,537
Variation Amount	27,808,531
Total Paid	123,311,921



The Project Concept is to enhance the experience of the existing water park in Al Montazah.

Components:

- Male / female changing rooms Restaurant , Cafee , Nurse room , Kids play area (Indoor and outdoor)
- Wave pool
- Multi- slides
- Theming concept
- The new target date to complete the development of water park on the 31st Jan. 2018 , and the green park on 15th Oct. 2018 (Including Shifting the wheel)

Key Project Milestones

Milestone	Due Date	Status
Concept Design		Done
Schematic Design		Done
Detailed Design		Done
Interior Design		Done
Construction Package		Done
Harding Installation & Artwork		N/A
Authority approval		Approval obtained from SEWA for additional 500 KVA in water park
Construction works		On going - Last stage (testing and Commissioning)
Landscape		On going
Lighting		On going (Flood Light and Theming light)
Public Furniture		By Al Montazah
CCTV		On going
Sound System		On going
FF&E		By Al Montazah (To check furniture for Fat and Elevation Burger
OS&E		By Al Montazah
Kitchen equipments		By Al Montazah
Signages & Wayfinding		By Al Montazah
Fire System		Finalized recently
SEWA /Authorities Connection		Approvals ottined , civil works on going
Snagging		On going for water park
Handover		Not started

Stakeholders List

Name	Impact	Status / Notes
Al Montazah Team	High	
Theming Contractor (ROCAS)	High	
Wheel works (Biscowice)	Medium	
Zampreia (Rides supplier)	High	
Internal Processes		
Responsible Department	Task	Status
Marketing	To Coordinate with All Montazah Team	
Public Relations	To Coordinate with All Montazah Team	
Government Relations	N/A	
Procurement	All project related items are under control	
Legal	Legal issue against Khuraif	
Business Development		
IT Technical Support	Supply and installation of Turnstiles	To be done before 10 th October. 2018
Property Management	To Coordinate with All Montazah Team	
Operation		
Finance	Some delays payment	Pushing to release it ASAP

A Green arrow in the checked column sheet filled by the approved document

FOR Chairman's Attention

Description	Urgency	Status
Legal case to be raised against M/S Kharaif		Ongoing
Rocas agreement		Ongoing
Items Related to operation by Al Montazah	High	On going
Delay of Rocas Works	High	On going

Risk	Impact	Indication	Mitigate
Action			
Operating the park without finalizing spare part agreement with Zampreia	Any defect in any spare part will affect the operation of the ride as it was not available in stock		Revised quotation received from Zampreia , and forwarded to Al Montazah to finalize
Over Budgeting due new scope of works required			
Delays in finalizing Kitchen Equipment in the Green Park			The installation contractor has been assigned
ROCAS Bad Quality of material supplied to site	Delay in project completion date		
Rocas agreement not yet finalized	relasing the payment without contractual support		
Operation items by al Montazah (Reception Counter , Service agreement with BISSWISS , Kitchen Equipment's)	Delay operation date		

Risk Table Per Project (Custom Form)



© 2013 CMCS FZCO







Enterprise Dashboard



General Projects Department
Enterprise Projects Dashboard

Owner: All Client: All Project Type: All

3,698M Budget Original	1,069M Budget This Year	143M Consultant Fee	2,412M Contract Value	111M Change Orders	2,523M Revised Contract	1,288M Paid To Date	-864M Pending Payment
Projects Status		Projects Issues Status		Budget This Year Spending			

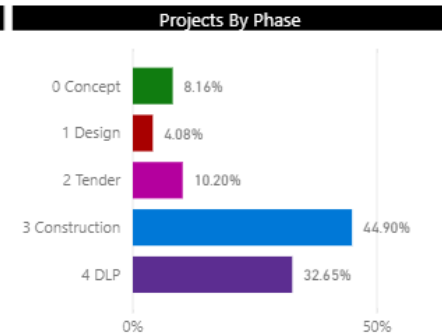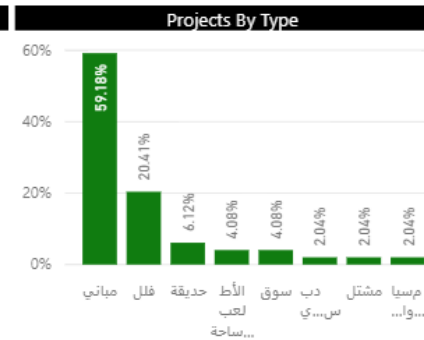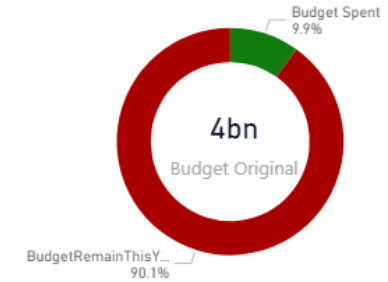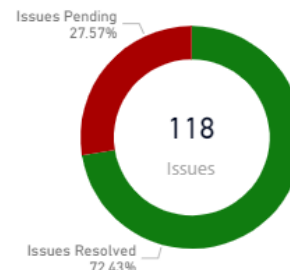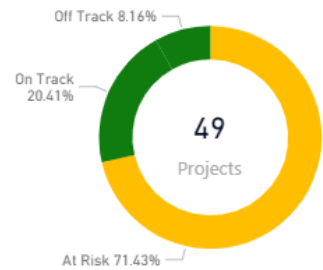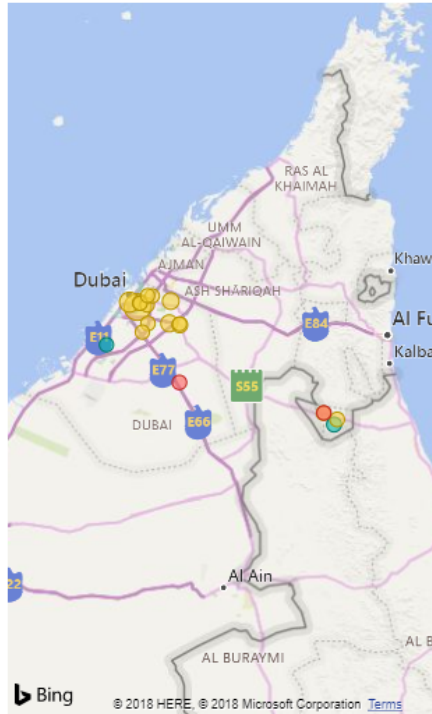

Projects Scorecard



General Projects Department
Enterprise Projects Scorecard

Owner: All Client: All Project type: All

3,698M		1,069M		143M		2,412M		111M		2,523M		1,288M		-864M			
Budget Original		Budget This Year		Consultant Fee		Contract Value		Change Orders		Revised Contract		Paid to Date		Pending Payment			
Project ID	Project Name	Planned Finish	Actual Finish	Budget Original	Contract Value	Change Orders	Revised Contract	% Planned	% Actual	Invoiced	Paid	Schedule	Scope	Quality	Issues	Cost	Safety
10111	مجمع الخدمات البيطرية	07/28/2016	09/18/2016	30,000,000	0	0	0	100.00%	100.00%	0	331,200						
10113	ورشة فرعية لإدارة النقلات بالليان	08/20/2016	08/29/2016	15,000,000	0	0	0	100.00%	100.00%	0	0						
10129	مشتل حنا	12/31/2017	12/25/2017	4,000,000	0	0	0	100.00%	100.00%	0	0						
10135	إنشاء مدفن هندسي للنفايات الخطرة	10/15/2018	12/30/2018	26,500,000	0	0	0	80.00%	80.00%	0	0						
10141	متحف دبي للآثار				0	0	0			0	0						
10145	مدينة المريخ العلمية			610,000,000	0	0	0			0	0						
20128	حديقة في عود المطينة الأولى	06/17/2018	06/25/2018	3,000,000	0	0	0	100.00%	100.00%	0	0						
30031	مبنى النيابة العامة الجديد	08/15/2018	03/03/2019	200,000,000	0	0	0	25.00%	25.00%	0	0						
30041	توسعة الحرم الجامعي لجامعة زايد	07/25/2018	07/08/2018	300,000,000	0	0	0	100.00%	100.00%	0	0						
30043	إستاد نادي شباب الأهلي - دبي بمنطقة الروية الثالثة	12/23/2018	12/23/2018	250,000,000	0	0	0	100.00%	100.00%	0	0						
30044	أعمال الديكورات الداخلية لمقر هيئة تنمية المجتمع			29,000,000	0	0	0			0	0						
10123	فيلا سيف محمد الرميثي	04/13/2018	04/13/2018	2,000,000	1,400,000	0	1,400,000	100.00%	100.00%	766,260	766,260						
10134	فيلا سيف عبد المهيري	06/17/2018	09/30/2018	2,000,000	2,000,000	0	2,000,000	100.00%	98.00%	766,260	766,260						
10130	فيلا على المر سعيد الكتيبي	03/13/2018	11/30/2018	1,000,000	2,140,000	0	2,140,000	94.00%	100.00%	558,205	558,205						
10127	فيلا خليفة محمد يافور محمد السيوسي	01/04/2019	01/04/2019	2,000,000	2,250,000	0	2,250,000	80.00%	80.00%	0	0						
10126	فيلا سالم محمد يافور محمد السيوسي	01/24/2019	01/22/2019	2,000,000	3,400,000	0	3,400,000	90.00%	90.00%	0	608,906						
10128	فيلا احمد محمد يافور محمد السيوسي	12/18/2017	09/30/2018	2,000,000	3,400,000	0	3,400,000	99.00%	100.00%	0	0						
10119	فيلا راشد محمد سعيد المهيري	06/27/2017	11/30/2018	2,000,000	3,470,000	0	3,470,000	100.00%	70.00%	0	0						
10124	فيلا السيد سعيد محمد مروشد	04/05/2018	12/30/2018	140,000	3,500,000	0	3,500,000	100.00%	52.00%	0	0						
10138	فيلا محمد سعيد محمد مروشد المهيري	01/14/2019	04/30/2019	2,000,000	3,750,000	0	3,750,000	71.00%	46.00%	0	0						
30023	جمعية النهضة النسائية في الليسيلي	08/20/2017	01/31/2019	5,000,000	6,575,154	0	6,575,154	100.00%	68.00%	3,777,635	3,777,635						

Project Charter Report – Part 1

This will be captured from the Project Form



PROJECT CHARTER- Fossil Rock Lodge (Mleiha)	
General Project Information	
Project Name	Fossil Rock Lodge
Project Manager	Abeer Al Hamdani
Budget	AED 20 M
Location	Mleiha
Affection Plan Availability	Not Available
Operator	MANTIS
Deadline	15th March 2018
Feasibility/market study	Not Available
Stakeholders	Shurooq, SRTA, SEWA, FEWA, DTPS
Describe the background, goals, objectives, and deliverables of this project	
Brief	
One of the main components of the Sharjah Collection is the Fossil Rock Lodge. Fossil Rock Lodge is located in Mleiha, Sharjah; it is approximately a ten minute drive from the Mleiha Visitor Center. The project is made up of three main components which are the lodge, the spa, and the F&B unit. Both the lodge and the F&B units are existing structures that date back to the 1960's. These structures have now been restored with minimal modern intervention apparent in the architecture. The interiors, however, are very contemporary in approach creating a unique juxtaposition of old and new. The currently existing petrol pump is regarded the first petrol pump in the UAE. Lastly, the spa is new addition that is meant to elevate the guests' experience ensuring an unforgettable stay at such a unique location of	
Components	
consisting of the lodge with 5 bedrooms, SPA and F&B building.	
Total Land	15118 m'
Area	
BUA	696 m'

Project Charter Report – Part 1

This will be captured from the Project Form



Project Schedule		
Key Milestone	Notes	
Design Completion	Completed	
Construction	01/15/18	
Pre-Opening	TBD (Mantis to advise)	
Define the Project Resources and Costs		
	Name	Department
Project Owner	Noora Lootah	Design Team
	Fadi Yousif	Construction
	Amal Taryam	ID
	Khawla Al Hashimi	Design
	Abeer Al Hamdani	Senior Project Coordinator
Deputy	Mai Barakat	Project Management
	Elie Armaly	Business Development
Other Departments	Ricardo	Special operations

Project Charter Report – Part 2

This data is captured from Awarded Commitments and Budget



Cost Type	Vendor / Client / Labor Names	Amount
Design Cost		
Architectural	Anarchitect	88,400.00
Arch & Interior Consult	Anarchitect	317,583.63
Architectural	Anarchitect	60,000.00
SPA Design	The Wellness	49,660.00
Landscape Design	Desert Ink	95,600.00
		611,243.63
Construction Cost		
Topographic Survey	Middle East Survey	7,500.00
Exterior Loose furniture	H&H Procurement	450,000.00
SPA Building	Alba Tower Aluminum Factory LLC	1,850,000.00
Supply & Instalation of B&B	Alba tower	3,331,000.00
Sanitary ware	Bagno Design LLC	29,067.00
Lights Supplier	Delta Light	379,451.76
Glass Work	Facade Solutions LLC	473,000.00
Sanitary Items	Kitchen and Bath Gallery General Trading LLC	158,110.00
Fit Out Contractor	Obaid Al Abdi Maint. and Decor LLC	5,480,000.00
SPA Equipment	The Wellness Technical Services Co LLC	1,875,430.00
Way Finding System	Skyne Branding	58,000.00
CCTV Live Camera system	Satin Audio Visual System LLC	12,900.00
MEP Contractor	OHM Star	582,000.00
Landscape Contractor	Desert Landscape Co. LLC	2,866,346.00
Procurement Service	Dimara	55,000.00
		18,830,292
Expected Cost (not signed yet)		
Cost Type	Vendor / Client / Labor Names	Amount
Connection fees	FEWA	1,350,000.00
Pre - Opening		413,129.00
OS&E	Dimara	754,965.00
		2,518,094.00

Project Charter Report – Part 3

Is it from Risk Register or Summary at Project Charter



69	Project Risks			
70	Risk			Impact
71	Delay in connection			Timeline
72	Kitchen requirement			Timeline
73	Street shifting by SRTA			Timeline
74				

Nominated Subcontractor Output Form (Custom Form to be Created)

PROJECT DEPARTMENT /NOMINATED SUB CONTRACTORS FORM			
		 شُرُوق SHUROOQ	
Date		Ref. Number	
Project			
Location			
Budget			
Scope of Work			
Sub-Contractor List			
S.NO	Sub Contractor Name	Price	Notes
Recommended Sub Contractor			
Name		Reason	
Attachments			
Quotations received from Subcontractors		Attached	
Approved Quotation (Signed)		Attached	
Approvals			
Construction Dept.	Project Dept.	Head of the Project	
Name & Signature	Name & Signature	Name & Signature	
H.E. Marwan bin Jassim Al Sarkal			
Chief Executive Officer			



Collaboration, Management and Control Solutions (CMCS)

EML: Bassam.Samman@CMCS-MENA.com

OFC: (+9714) 365-4850 LINKEDIN: [Bassam.Samman](#) WEB: www.CMCS.co
